

## Record of Water Service Connection

PROJECT: Lead Service Replacement Program-Phase I, New Bedford, MA

STREET: Nelson Street

HOUSE No: 69

Contractor: P Gioioso and Sons, Hyde Park, MA

Date: 7/29/2020

Type: Copper Diameter (in): 1"

Distance from main to curb stop (ft): 21.5 Water Pressure (PSI) 100

Distance curb stop to meter (ft): 14

Distance from curb face to curb stop (ft): 0.9

Depth of Service (ft): 4.5


Total length of new pipe installed (ft): 23

Curb Stop Replaced: yes Size (in): 1

Corporation Replaced: yes Size (in): 1

Ball Valve Replaced: no Size (in): 3/4

Ties:

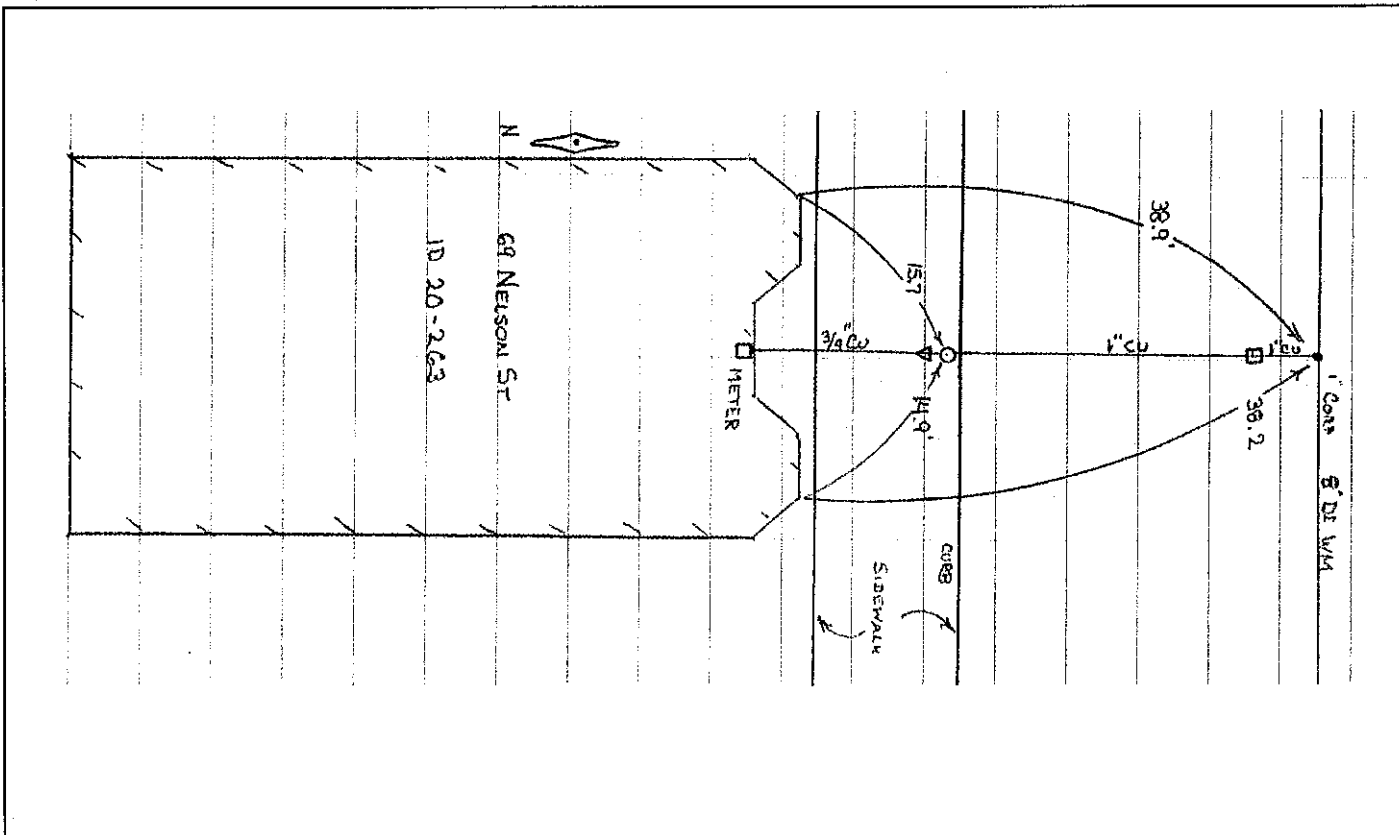

Remarks:

1" union installed where shown  
1-3/4" union installed where shown
