

Record of Water Service Connection

PROJECT: LEAD SERVICE LINE REPLACEMENT PROGRAM - PHASE II

SERVICE ID: 10200 ADDRESS: 22 STREET: LUCAS STREET

CONTRACTOR: C. NAUGHTON CORP DATE: JULY 15, 2024

TYPE:

FULL (MAIN TO METER): ☐

PARTIAL (MAIN TO CURB STOP): ☒

PARTIAL (CURB STOP TO METER): ☐

MEASUREMENTS:

MAIN TO CURB STOP: 10.0'

CURB STOP TO METER: 2.0

CURB FACE TO CURB STOP: 1.3'

SERVICE DEPTH: 4.2'


WATER PRESSURE: 78 PSI

SERVICE LINE REPLACEMENT:

	(YES/NO)	SIZE	MATERIAL
SERVICE LINE (MAIN TO CS):	YES	1"	COPPER
SERVICE LINE (CS TO METER):	NO		COPPER
CORPORATION:	YES	1"	
CURB STOP:	YES	1"	
BALL VALVE:	NO		
METER:	NO		

SERIAL NUMBER: N/A

TIES:

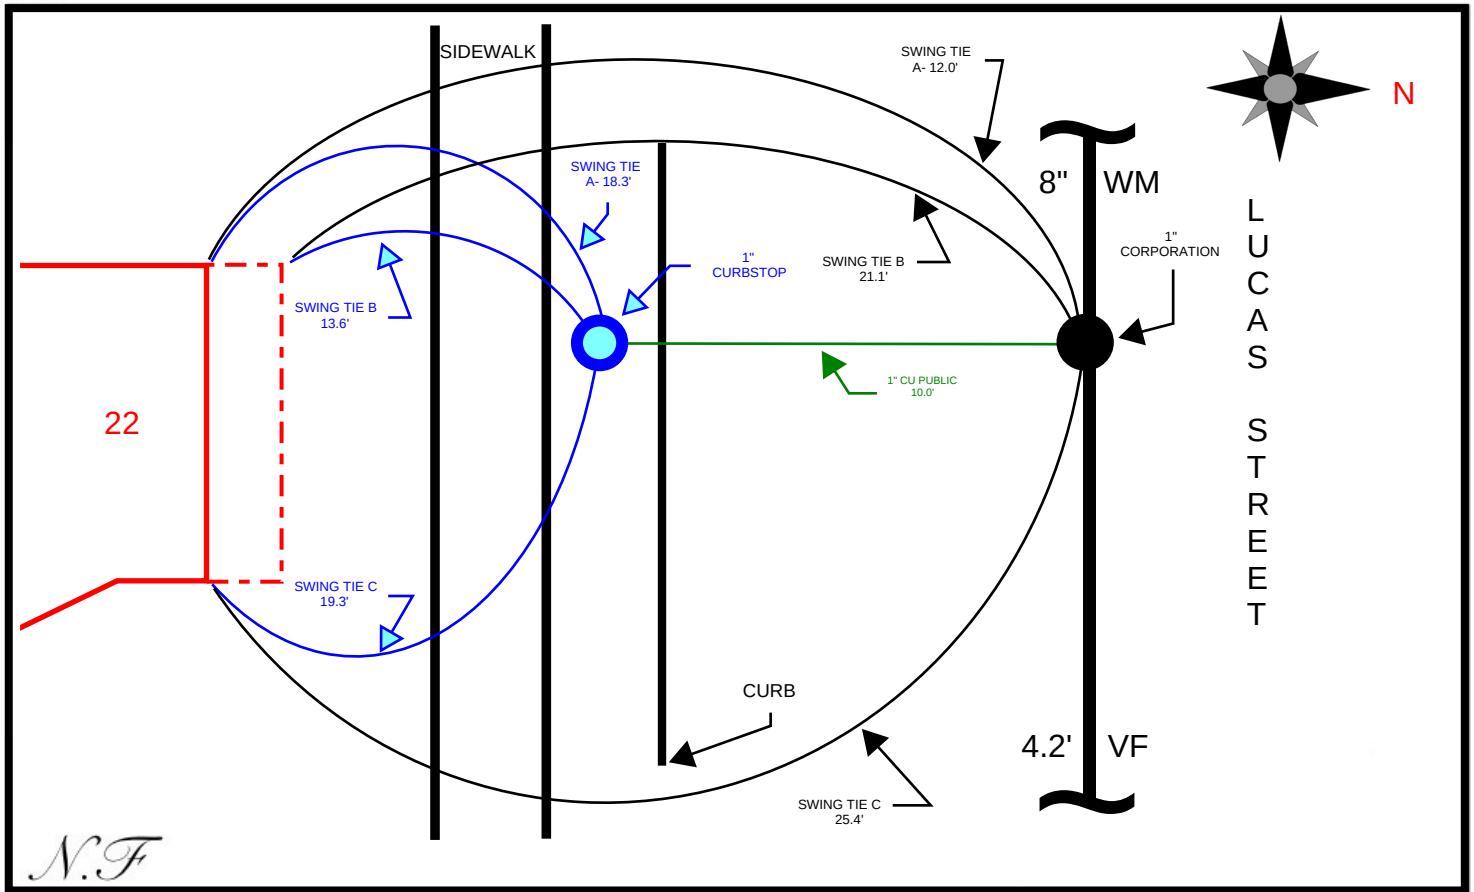

Remarks:

3/4" X 1" UNION INSTALLED WITHIN 2.0' SOUTH OF CURB STOP

APPLICATION No.: 10200 C

TAP CLEARED

LOCATION: Rear 22 Lucas

OWNER: _____

MEASURES: $\frac{1}{2}$ "

INACTIVE SER

DATE

BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

[illegible]
