

APPLICATION No.: 10496

LOCATION: 22 Viall St

TAP CLEARED

OWNER:

31-313

MEASURES: 4/10/2019 1" Copper Service  
Lead Service Line Replacement Program  
Phase 1, Contractor P Gioioso & Son  
Type CU, Diameter 1in, Water pressure 100  
Distance from main to curb stop (ft) 23  
Distance curb stop to meter (ft) N/A  
Distance from curb face to curb stop (ft) 1  
Depth of service (ft) 4  
Total length of new pipe installed (ft) 23  
Curb stop replaced: Yes size 1"  
Corporation replaced: Yes size 1"  
Ball valve replaced: No

DATE


BEF.

AFT.

REMARKS

[illegible]

### CHARGE OUTS<sup>11</sup>

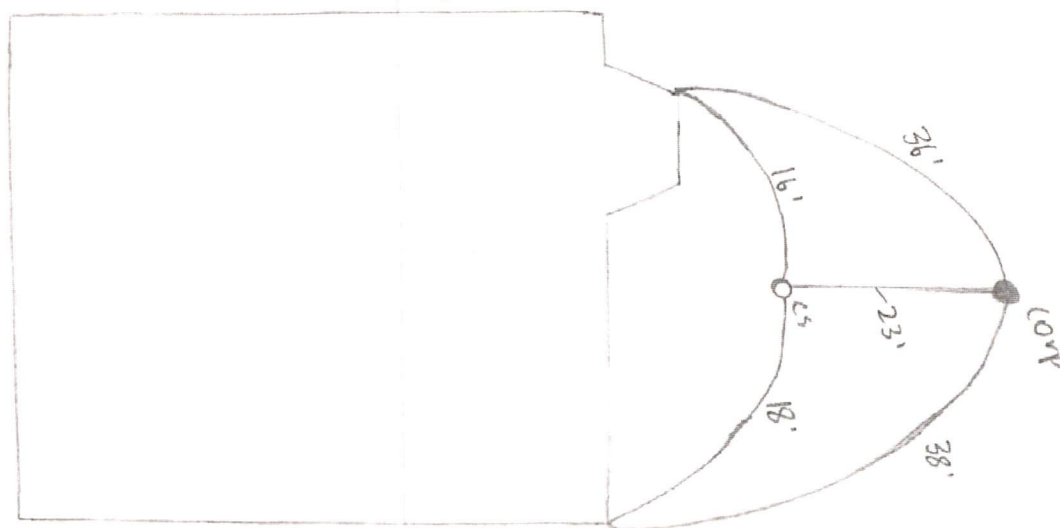

John Martin 993 941

APPLICATION No.: 10496

TAP CLEARED 8645-382

LOCATION: 22 V1011

OWNER: J & DH Duehsworth 26

MEASURES:  $\frac{1}{2}$ "

N from  
W from E  
S from N

Ruth  
Viall  
house

332.9 ft.

8.5 ft.

11.0 ft.

8/2/86: Renewed from 1/2' outside curb stop to prop line.

Stock: 7ft. 3/4" copper tubing 1 - 3/4" curb stop 1 - caldwell  
stop box 2 - 3/4 x 5/8 lead to cop adapt. xs.

OWNER WOULD LIKE RENEWAL  
WAS TOLD TO CHECK WITH US LATER IN YEAR  
(TOO HEAVY WORK LOAD) J.R.

11/7/86: JRenewed from main to a point 1 ft. Stock: 1ft. - 3/4" copper tubing 1 - 3/4 x 5/8 lead to cop adapt. xxs 1 - 3/4 x 5/8

NOTE: 5/8" tap not 1/2" =====

2/25/87: Renewed from 1/2' outside curb stop to inside cellar.  
Stock: 14ft. 3/4" copper tubing (8' ins.)

[illegible]



[illegible]

CHARGE OUTS.
