

APPLICATION No.: 10751

LOCATION: 114 South St

OWNER:

31-313

MEASURES: 1" Copper Service

08/28/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 24

Distance from curb face to curb stop (ft) 2

Depth of service (ft) 4.5

Total length of new pipe installed (ft) 24

Curb stop replaced: NO, Corporation replaced: NO

Ball valve furnished: Yes size 1"

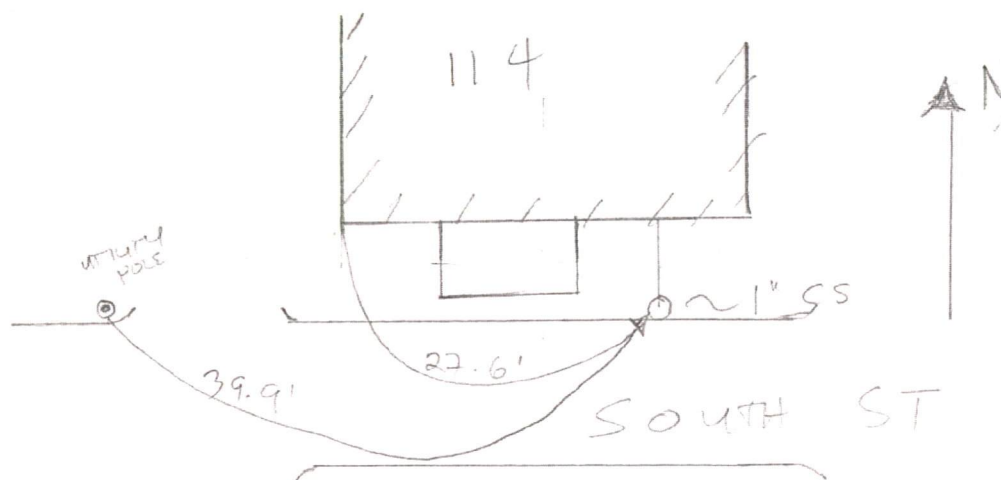
TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

[illegible]

APPLICATION No.: 10751

TAP CLEARED

12-4
8649 2381

LOCATION: 114 South St.

OWNER: Luiz Da S. Gonsalves

MEASURES:

5/8" H lead May 26, 1904

E from Crapo St. 184.5 ft.

N from S line South St. 9.3 ft.

E from W line house 4.0 ft.

12/5/86: Renewed from main to a point 2.0 ft. Stock: 2.0ft.

3/4" copper tubing 1-3/4x5/8 lead to cop adapt. xxs

1 - 5/8 Fig. 413

07/23/13

City crew renewed service from main to property line.

Stock: 17ft - 3/4" copper tubing; 1 - 3/4" curb stop;

1 Caldwell stop box; 1 - 5/8"x3/4" XXS Lead to cop

adapt; 1 - 5/8"x3/4" Fig 413; Tap reamed.

J. Medeiros

DATE

BEF.

AFT.

REMARKS

12/5/86 TAP REAMED

7/23/13

Tap reamed
2013-3003361

[illegible]
