

11020

LOCATION: 133 Fair St

OWNER:

31-313

MEASURES: 10/05/2018

1" Copper Service

Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) N/A

Distance curb stop to meter (ft) 18

Distance from curb face to curb stop (ft)2

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 18

Curb stop replaced: no

Corporation replaced: no

Ball valve furnished: yes, size 1"

TAP CLEARED

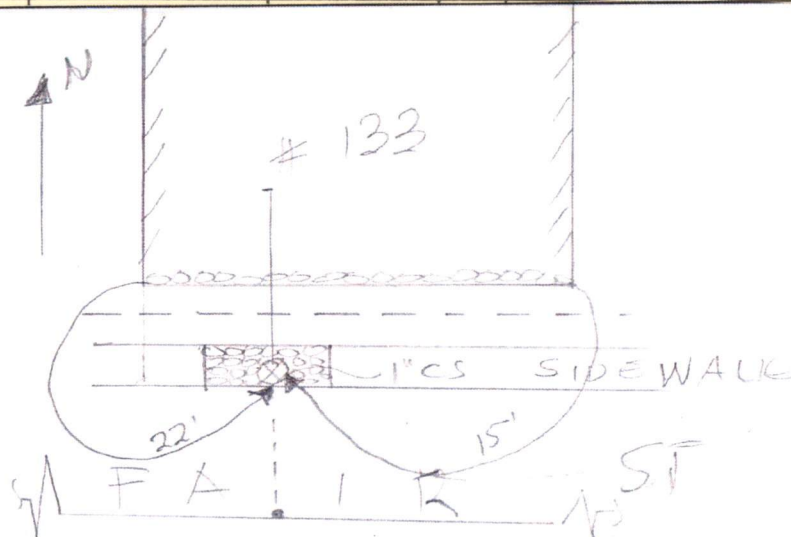
DATE _____

BEF.

AFT.

REMARKS

[illegible]

[illegible]

APPLICATION No.: 11020TAP CLEARED 8509-2736LOCATION: 133 Fair St.OWNER: Manuel SylviaMEASURES: 5/8" H lead May 10, 1905W from Briggs St. 82.5 ft.S from N line- Fair St. 9.0 ft.W from EAline house 4.0 ft.

3/1/85: Renewed from 1/2' outside cutb stop to prop line

Stock: 6ft. 1" 3/4" copper tubing 1 3/4' curb stop

1 Caldwell stop box 2 3/4x5/8 lead to cop adapt. xxs

=====

10/23/91: Renewed from main to curb stop

Stock: 22ft. 3/4" copper tubing same curb stop

same Caldwell stop box 1-3/4x5/8 Fig. 413

DATE

BEF.

AFT.

REMARKS

9143 300110/23/91: TAP REAMED

[illegible]

CHARGE OUTS

[illegible]
