

APPLICATION No.: 11134

LOCATION: 392 Cottage St

TAP CLEARED ✓

OWNER: _____

31-313

MEASURES: Aug. 3, 1905

N from Sycamore St 84.5 ft

W from E line Cottage St 7.0ft

N from S line House 12.2 ft

1" Copper Service

03/24/2020 Lead Service Line Replacement Program

Phase 1 Contractor P Gioioso and Son

Type CU, Diameter (in) 1, Water Pressure 55

Distance from main to curb stop (ft) 23.6

Distance from curb stop to meter (ft) 10

Distance from curb face to curb stop (ft) 2.4

Depth of service (ft) 3.3

Total length of new pipe installed (ft) 33.6

Curb stop replaced: yes, size 1"

Corporation replaced: yes, size 1"

Ball Valve replaced: yes, size 1"

DATE

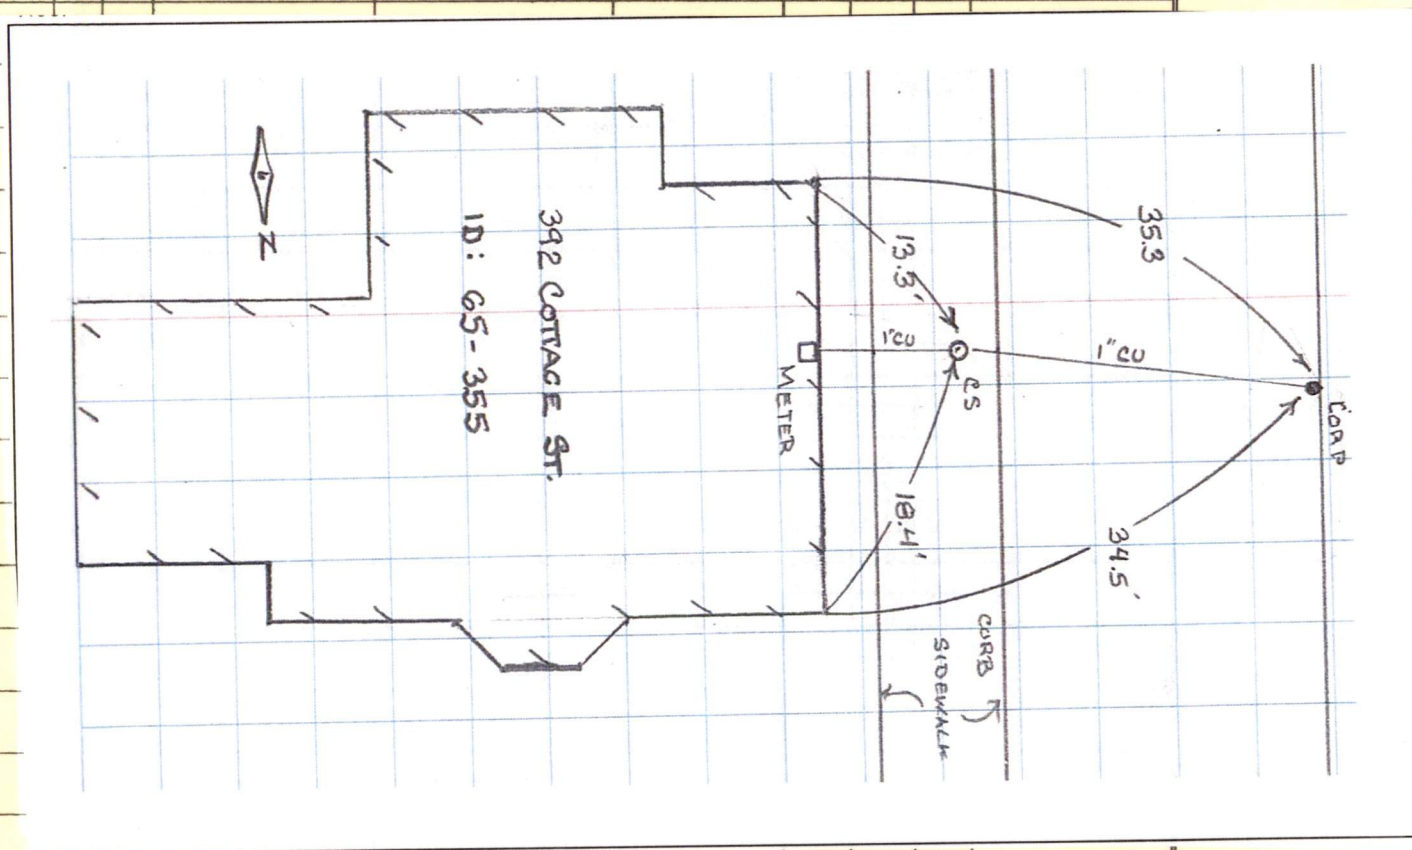
BEF.

AFT.

REMARKS

[illegible][illegible]

CHARGE OUTS

[illegible]
