

APPLICATION No.:

LOCATION:

OWNER:

APPENDICES

Measures:	5/8"		
W from	Acushnet Ave	55'	
S from N line	Clifford	9.5'	
W from E line	House	4.0'	

1" Copper Service

08/25/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 24'

Distance from curb stop to meter 15.5'

Distance curb face to curb stop 1.5'

Depth of Service 4.50'

Total length of new pipe installed 39.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes 1"

Remarks: Type C 1" Copper to meter, 7" Lead removed.

TAP CLEARED

DATE _____

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

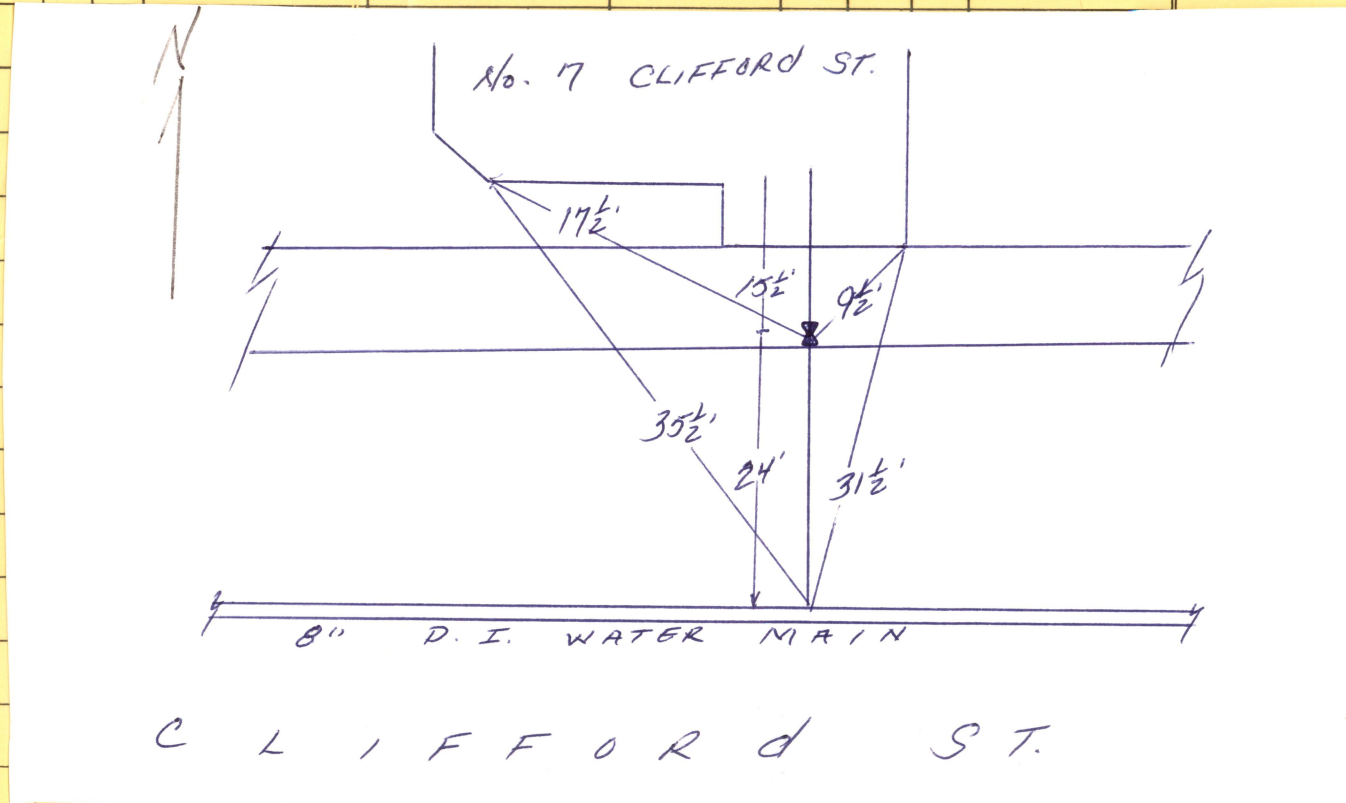

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: CLIFFORD ST.

HOUSE No: 7

Contractor: C. Naughton Corp.

Date: 8-25-22

Type: CU Diameter (in): 1

Distance from main to curb stop (ft): 24'

Distance curb stop to meter (ft): 15½'

Distance from curb face to curb stop (ft): 1½'

Depth of Service (ft): 4½'


Total length of new pipe installed (ft): 39½'

Curb Stop Replaced: Yes Size (in): 1

Corpration Replaced: Yes Size (in): 1

Ball Valve Replaced: Size (in): 1

Ties:

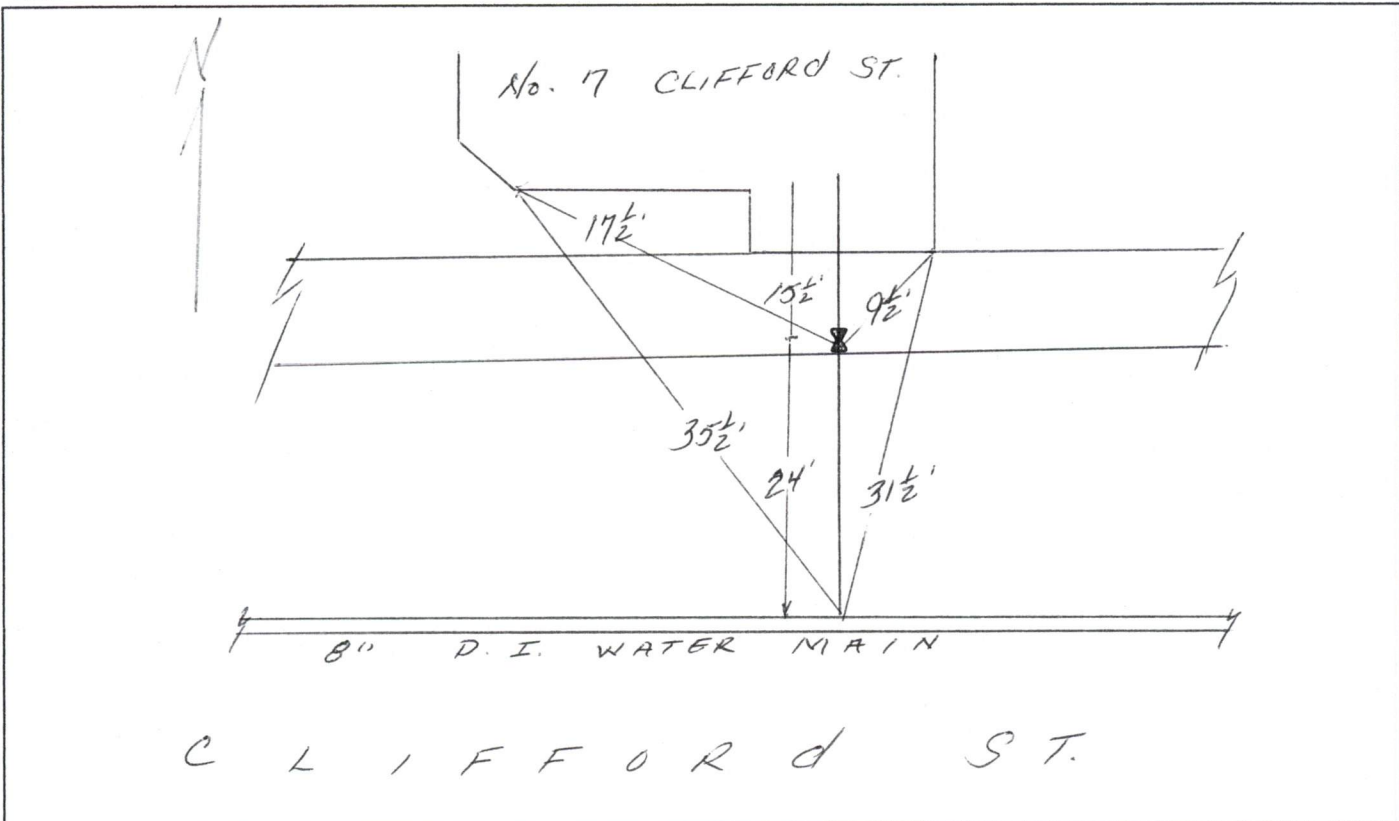

Remarks:

TYPE C - 1" COPPER TO METER, 7' LEAD REMOVED.
