

✓ APPLICATION No.: 11785

LOCATION: 31 Viall St

TAP CLEARED

OWNER: _____

31-313

MEASURES: 4/9/2019 1" Copper Service
Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 100
Distance from main to curb stop (ft) 10
Distance from curb stop to meter (ft) N/A
Distance from curb face to curb stop (ft) 2
Depth of service (ft) 4
Total length of new pipe installed (ft) 10
Curb stop replaced: Yes size 1"
Corporation replaced: Yes size 1"
Ball valve replaced: No

DATE

BEF.


AFT.

REMARKS

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

CHARGE OUTS

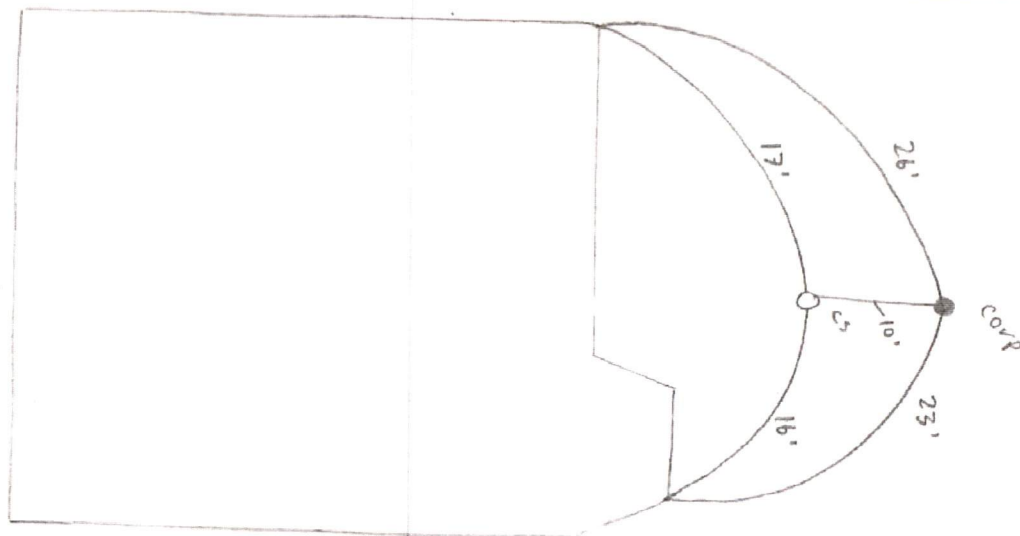

APPLICATION No.: 11785

TAP CLEARED

LOCATION: 31 ViallOWNER: Thos NizukMEASURES: 5/8"

N from	Ruth	129.0 ft.
E from W line	Viall	8.7 ft.
S from N line	house	10.4 ft.

Load in trech with drain.

5-13-99 Renewed from main to inside cellar. (5 ft. ins. prop. line) Stock: 13 ft. - 3/4" Copper tubing, 1 - 3/4" x 3/4" Curb Stop, 1 - 5/8" x 3/4" Fig. 413.

4/21/99 MAYBE LEAD NOTICE

ARUJO BROS. PLUMMING

DATE

BEF.

AFT.

REMARKS

5-13-99 Tap reamed

[illegible]
