

APPLICATION No.: 11897

TAP CLEARED

LOCATION: 296 Earle St

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: 06/20/2018 Lead Service Line Replacement Program

Contractor P Gioioso & Son, Phase 1

Type CU, Diameter 1in, Water pressure 70

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 13.0

12.0 to house - 1 wall

Distance from curb face to curb stop (ft) 1.5

Depth of service (ft) 3.5

Total length of new pipe installed (ft) 16.0

13 ft + 3 ft whip


Curb stop replaced: no,

Corporation replaced: no

Ball Valve Furnished: yes size 1"

[illegible]

CHARGE OUTS

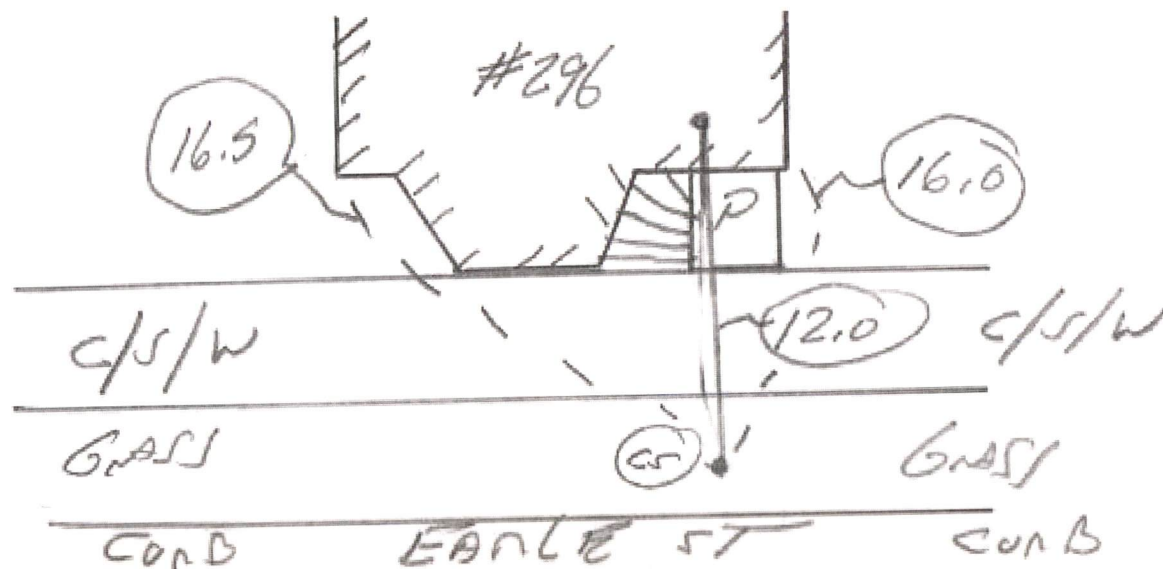

APPLICATION No.: 11897

LOCATION: 296 Earle

OWNER: Michael Jau p

MEASURES:

5/8"

W from	Ashley Blvd.	330.2
N from S line	Earle	8.8
E from W line	House	10.7

Nov. 15, 1954 Renewed from a point $\frac{1}{2}$ ft. outside curb stop to a
point 2 ft. inside curb stop $2\frac{1}{2}$ ft. of $\frac{3}{4}$ " copper tubing
 $\frac{3}{4}$ " copper stop, fig. 415 2 wiped joints.

12/22/97: Renewed from 1/2' outside curb stop to prop. line.
Stock: 7.5 ft. 3/4" copper tubing, 1- 3/4" curb stop, 1- #1
Caldwell stop box, 2- 5/8x3/4 lead to cop. adapt.xxs

1/9/04 Renewed from main to curb stop. Stock: 8 ft. 3/4" copper tubing; 3/4" curb stop; Caldwell stop box; 5/8" x 3/4" Fig. 413 Tap reamed

TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

12/24/92

975200658

1/9/04

930 AM

2004-020-4333

1/9/04

Tap reamed	
------------	--

[illegible]

CHARGE OUTS

[illegible]
