

11939

LOCATION: 258 Tinkham St

**OWNER:**

31-313

MEASURES: 1" Copper Service 05/23/2018  
Lead Service Line Replacement Program  
Phase 1, Contractor P Gioioso & Son  
Type CU, Diameter 1in, Water pressure 70  
Distance from main to curb stop (Ft) N/A  
Distance from curb stop to meter (Ft) 14  
Distance from curb face to curb stop (ft) 2.5  
Depth of service (ft) 5  
Total length of new pipe installed (ft) 17  
Curb stop replaced: No  
Corporation replaced: No  
Ball valve replaced: Yes size 1"

TAP CLEARED

DATE \_\_\_\_\_

BEF.


AFT.

REMARKS

[illegible]

[illegible]

### CHARGE OUTS

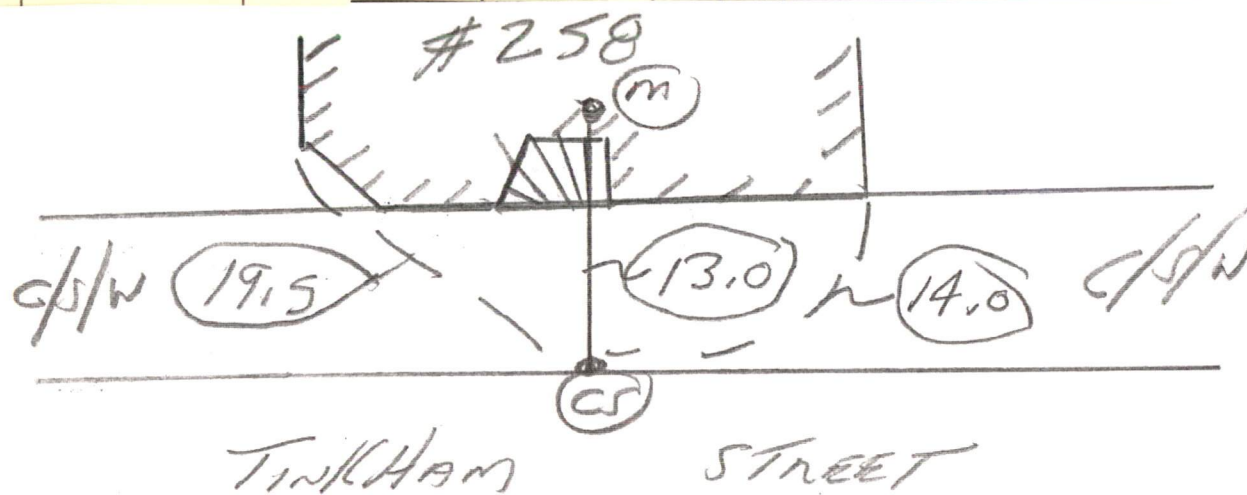

APPLICATION No.: 11939

TAP CLEARED ✓

LOCATION: 258 TinkhamOWNER: Walter J. HamotMEASURES: 5/8"

W from	Ashley Blvd.	261.0 ft.
N from S line	Tinkham	9.5 ft.
E from W line	house	11.0 ft.

-----  
December 31, 1963 Renewed from main to 3 ft. from main.  
3 ft. of 3/4" copper tubing 1 lb. wiping solder  
1 5/8" reused corporation coupling

-----  
January 6, 1951 Renewed from curb stop to middle of sidewalk.  
3 ft. of copper tubing

-----  
Dec. 22, 1975 Renewed from 1 ft. outside curb stop to 2 ft.  
inside.  
3 ft. 3/4" copper tubing 1 3/4" curb stop  
1 Caldwell stop box 2 5/8" x 3/4" lead to cop.adapt. XS

-----  
2005 earle st sewer project 3/4 copper main-prop line

DATE	BEF.	AFT.	REMARKS
------	------	------	---------

12-31-63

Reamed



[illegible]

CHARGE OUTS
