

APPLICATION No.: 12172

LOCATION: 324 Earle St

OWNER:

31-313

MEASURES: 06/19/2018 - Lead Service Line Replacement Program, Phase 1, Contractor P. Gioioso & Son
Type CU, Diameter 1in, Water pressure 70
Distance from main to curb stop (ft) N/A
Distance from curb stop to meter (ft) 13.0 ft
12.0 ft to house + 1 ft wall
Distance from curb face to curb stop 1.0
Depth of service (ft) 3.4
Total length of new pipe installed 16.0
13 ft + 3 ft whip
Curb stop replaced: no, size 3/4"
Corporation replaced: no, size 3/4"
Ball valve furnished: yes, size 1"

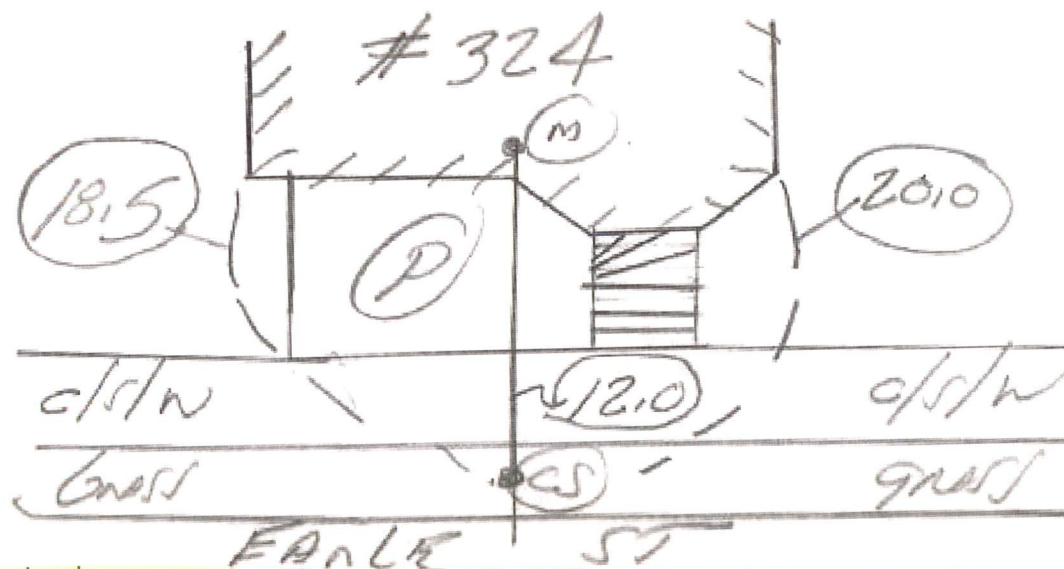
TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

[illegible]

APPLICATION No.: 12172

TAP CLEARED 84010454

LOCATION: 324 Earle
OWNER: R&S.A. Medeiros

MEASURES:

5/8"

E from	Brook	20.5
N from S line	Earle	9.0
W from E line	House	11.4

Jan. 5, 1984 - Renewed 1 ft. outside curb stop to property line.

6 ft. - 3/4" copper tubing

1 - 3/4" curb stop 1 stop box

2 - 5/8" x 3/4" lead to copper adaptors XS

- - - - -

2005 Earle St sewer project 3/4 copper main - prop line

DATE

BEF.

AFT.

REMARKS



[illegible]

CHARGE OUTS

[illegible]
