

APPLICATION No.: 12390 5/8" L lead

TAP CLEARED

LOCATION: 104 Clifford St. E. of Arlington St.

OWNER: Philias Duchaine

DATE

BEF.

AFT.

REMARKS

7/11/73

Reamed

MEASURES:	5/8"	L lead	Nov. 20, 1908
	E from	Arlington	247.8 ft.
	N from S line	Clifford	8.0 ft.
	E from W line	House	4.0 ft.

July 11, 1973 Renewed from the main to inside cellar.
31 ft. - 3/4" Copper tubing (13 ft. inside)
3/4" Hays curb stop 5/8" x 3/4" Fig. 413 cplg.

1" Copper Service

09/01/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 9.5'

Distance from curb stop to meter N/A

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 15'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"


Ball Valve replaced yes N/A

Remarks: Type B - Connect to 3/4" Copper @ PL.

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS
4/17/63		5/8	Calmet	16640063					

CHARGE OUTS

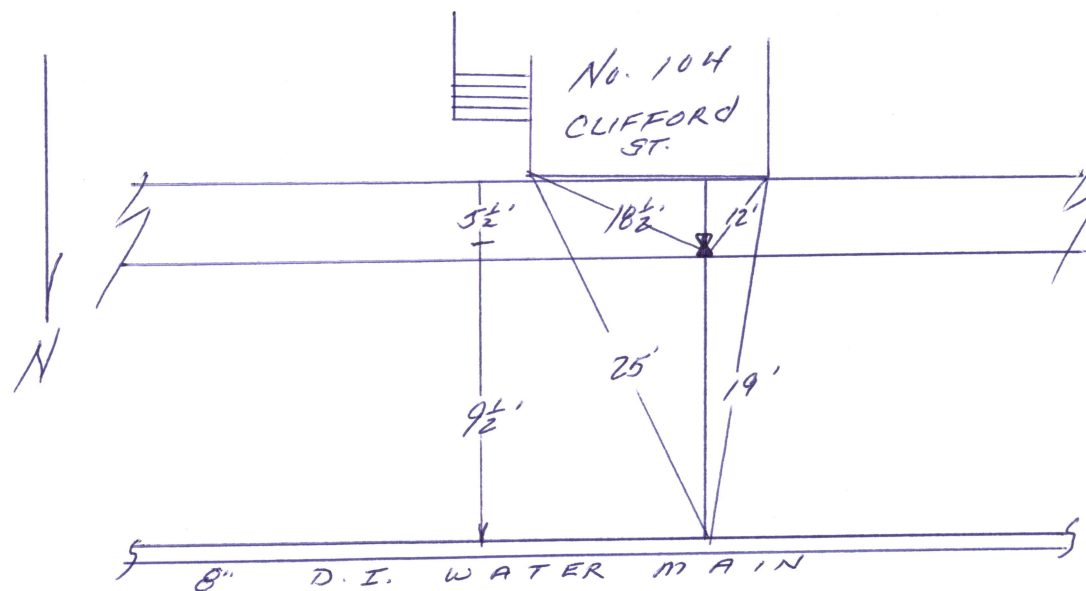

C L I F F O R D ST.
