

APPLICATION No.: 12495

LOCATION: 278 Tinkham St

OWNER:

31-313

MEASURES: 1" Copper Service 05/29/2018
Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 70
Distance from main to curb stop (ft) N/A
Distance from curb stop to meter (Ft) 17.5
Distance from curb face to curb stop (Ft) 1
Depth of service (ft) 3.4
Total length of new pipe installed (Ft) 20.5
Curb stop replaced: NO
Corporation replaced: No
Ball valve replaced: Yes size 1"

TAP CLEARED

DATE _____


BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

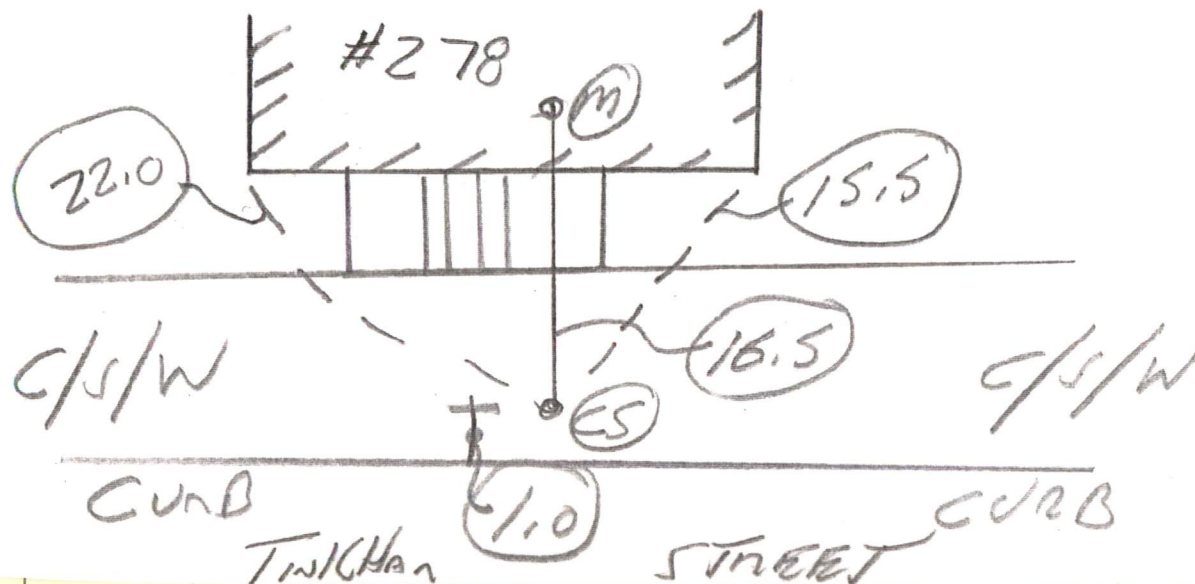

APPLICATION No.: 12495

TAP CLEARED ✓

LOCATION: 278 Tinkham

OWNER: Henry J. Wareing

MEASURES: 5/8"

E from Brook 160.0 ft.

N from S line Tinkham 9.0 ft.

E from W line house 5.4 ft.

DATE

BEF.

AFT.

REMARKS

12/20/95: tap reamed

2/20/96

960800399

ELECTRIC-CLEAN

2/20/96: tap reamed

 December 20, 1954 Renewed from a point $\frac{1}{2}$ ft. outside curb stop
 to a point $3\frac{1}{2}$ ft. inside the curb stop.

4 ft. of 3/4" copper tubing 1 3/4" copper stop

2 wipe joints

Dec 20, 1995: RENEWED from 1ft outside curb stop to prop line
 Stock: 7ft 3/4" copper tubing 1-3/4" curb stop
 1- Caldwell stop box 2-3/4 x 5/8 lead-cop adapt. xs

=====

Feb 20, 1996: RENEWED from main to a point 4ft
 Stock: 4ft 3/4" copper tubing 1-3/4x5/8 lead-cop adapt.xs
 1 - 3/4x5/8 Fig 413

=====

2005 Earle St sewer project 3/4 copper main-prop line

[illegible]
