

APPLICATION No.: 12651

TAP CLEARED

LOCATION: 19 Fair St

OWNER:


31-313

MEASURES: 09/17/2018 Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son
1" Copper Service
Type CU, Diameter 1in, Water pressure 100
Distance curb stop to main (ft) 28.5
Distance curb stop to meter (ft) N/A
Distance curb face to curb stop (ft) 2
Depth of service (ft) 5.5
Total length of new pipe installed (ft) 28.5
Curb stop replaced: yes, size 1"
Corporation replaced: yes, size 1"
Ball valve furnished: no

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

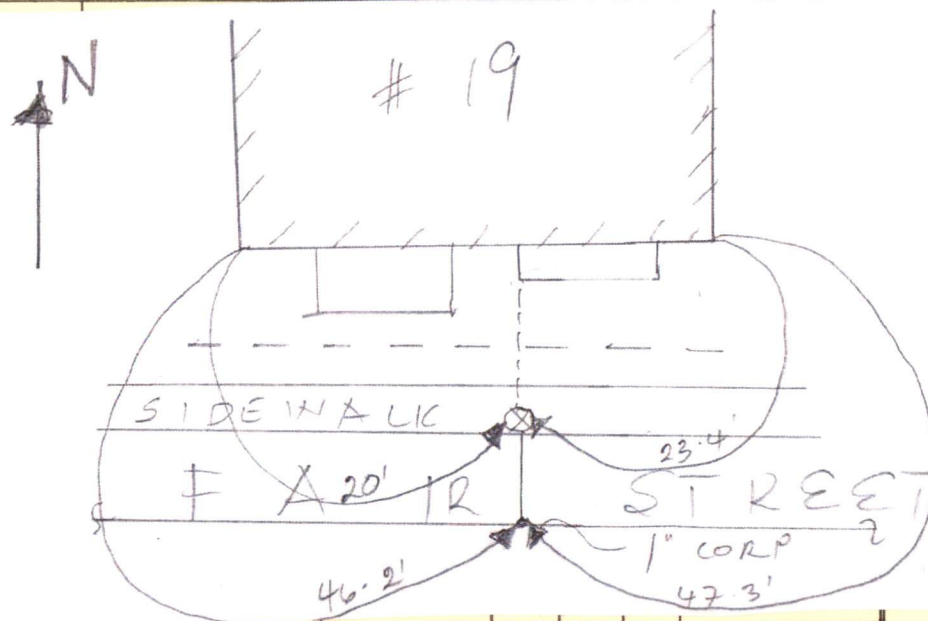

APPLICATION No.: 12651TAP CLEARED L 3039 ✓LOCATION: 19 Fair St.OWNER: Americo A. Baldo

MEASURES:

5/8" H lead May 3, 1909

W from County St. 185.5 ft.

S from N line Fair St. 8.0 ft.

E from W line house 10.0 ft.

DEC 22 1981 - Renewed from 1 ft. outside curbstop to the
property line. 9.0 ft. - 3/4" copper; 3/4" curb stop; stop
box; 2- 5/8" x 3/4" lead-cop. adapt. XXS;

10/06/09 - Renewal - New Measures:

W from W line County St	185.5
S from N line Fair St	8.5
E from W line House	10.0
W from E line House	18.0
S from S line House	17.0
Main to Property Line	35.0
Pipe inside property	10.0

10/6/09 - Dennis Trucking renewed service from curb stop
to meter . Owner charged \$130(\$30- shut-off, \$70 -inspection
and \$30 -turn-on) Inspected by Percy Reynolds

[illegible]

CHARGE OUTS.

[illegible]
