

APPLICATION No.: 12866

LOCATION: 300 Earle St

OWNER:

31-313

MEASURES: 06/20/2018 - Lead Service Line Replacement  
Program, Phase 1, Contractor P Gioioso & Son  
Type CU, Diameter 1in, Water pressure 70  
Distance from main to curb stop (ft) N/A  
Distance from curb stop to meter (ft) 19.5  
18.5 ft to house + 1 ft wall  
Distance from curb face to curb stop (ft) 2.0  
Depth of service (ft) 3.5  
Total length of new pipe installed (ft) 22.5  
19.5 + 3 ft whip  
Curb stop replaced: no  
Corporation replaced: no  
Ball Valve Furnished: Yes, size 1"

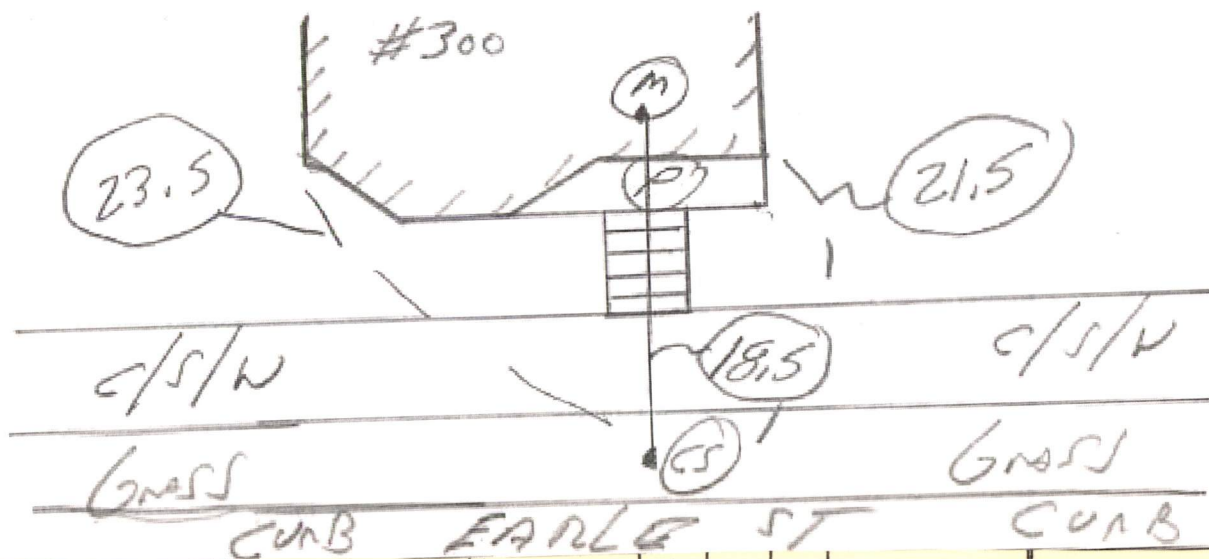
TAP CLEARED

DATE \_\_\_\_\_

BEF.

AFT.

REMARKS

[illegible]



103

APPLICATION No.: 12866

TAP CLEARED 87443619

LOCATION: 300 Earle  
 OWNER: A. Wronaetrix

MEASURES:

5/8"

E from	Brook	263.6
N from S line	Earle	8.8
E from Wline	House	11.5

10-29-87 Renewed from 1/2' outside curb stop to prop line  
 10ft-3/4" copper tubing, 1-3/4" curb stop, 1-Caldwell stop box  
 2-5/8x3/4 lead to cop adapt xs

11/20/87: Renewed from main to curb stop.

Stock: 8ft. 3/4" copper tubing 1-3/4x5/8 Fig. 413

1 - 5/8 x 3/4 corporation tap 1-6" x 3/4" service saddle.

=====

11-17-98 Renewed from 1/2' outside prop. line. Stock:  
 3 ft. - 3/4" Copper tubing, 1 - 3/4" x 3/4" cop. to cop  
 cplg., comp.

DATE

BEF.

AFT.

REMARKS

✓

8747-3824

11-24-98

984802185

[illegible]

## CHARGE OUTS

[illegible]
