

APPLICATION No.: 13018

TAP CLEARED

LOCATION: 301 Davis St

OWNER:

31-313

MEASURES:

E X Brook St 265.3 ft

S X N Line Davis St 8.5 ft

E X W Line House 13.2 ft

1" Copper Service

06/06/2018 Lead Service Line Replacement

Program, PHase 1, Contractor P Gioioso & Son

Type CU, Diameter (in) 1, Water pressure 55

Distance from main to curb stop (ft) 26.0

Distance from curb stop to meter (ft) 19.0

Distance from curb face to curb stop (ft) 2.0

Depth of service (ft) 3.5

Total length of new pipe installed (ft) 48

Public 26.0 ft Private 22.0 ft

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

Ball Valve furnished: yes size 1"

Remarks: 26.0 ft corp to curb stop 18.0 ft curb

stop to house 1.0 ft house to meter 3.0 ft

Whip

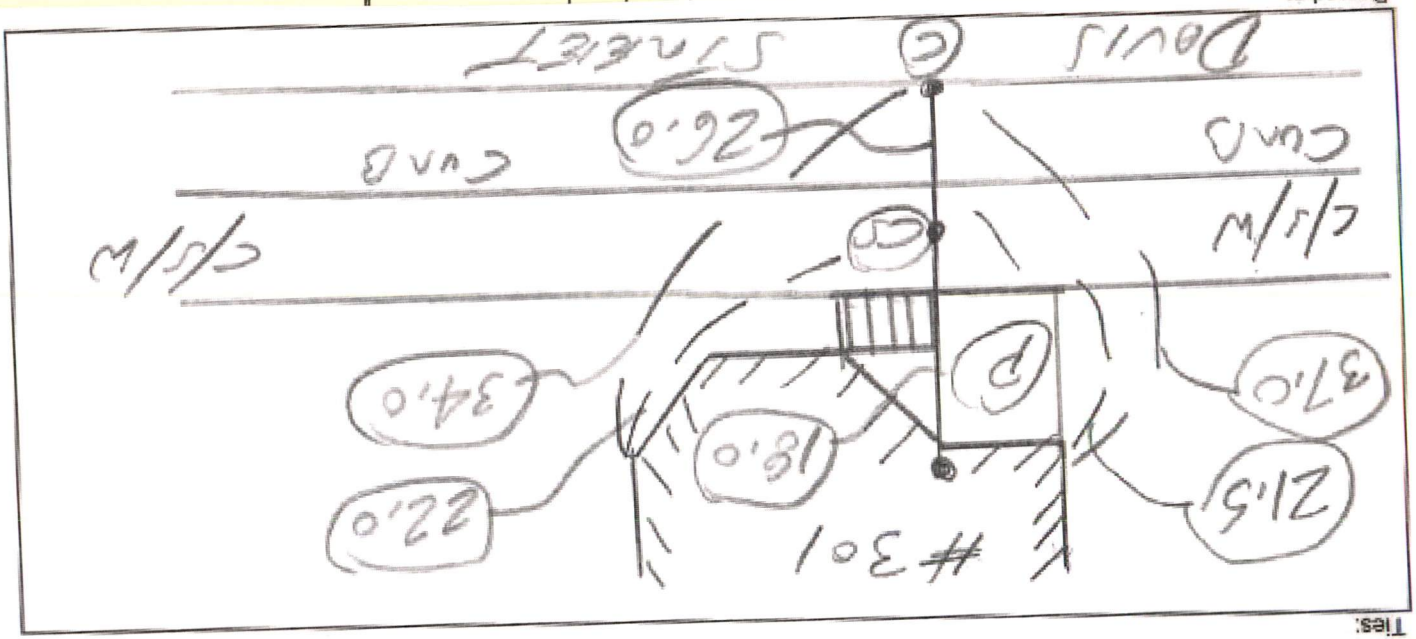
DATE

BEF.

AFT.

REMARKS

12/26/86 Reamed

[illegible][illegible]

Remarks:
