

APPLICATION No.: 13105

## TAP CLEARED

LOCATION: 210 Eugenia St

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

## MEASURES:

1" Copper Service

04/04/2018 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso &amp; Son

Type CU, Diameter 1in, Water pressure 59

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 16.0

Distance from curb face to curb stop (ft) 2.3

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 19.0

Curb stop replaced: No

Corporation replaced: No


Ball valve furnished: yes, size 1"

Remarks: 15.0 ft curb stop to house, 1.0 ft wall thickness

3.0 ft whip

[illegible]

### CHARGE OUTS

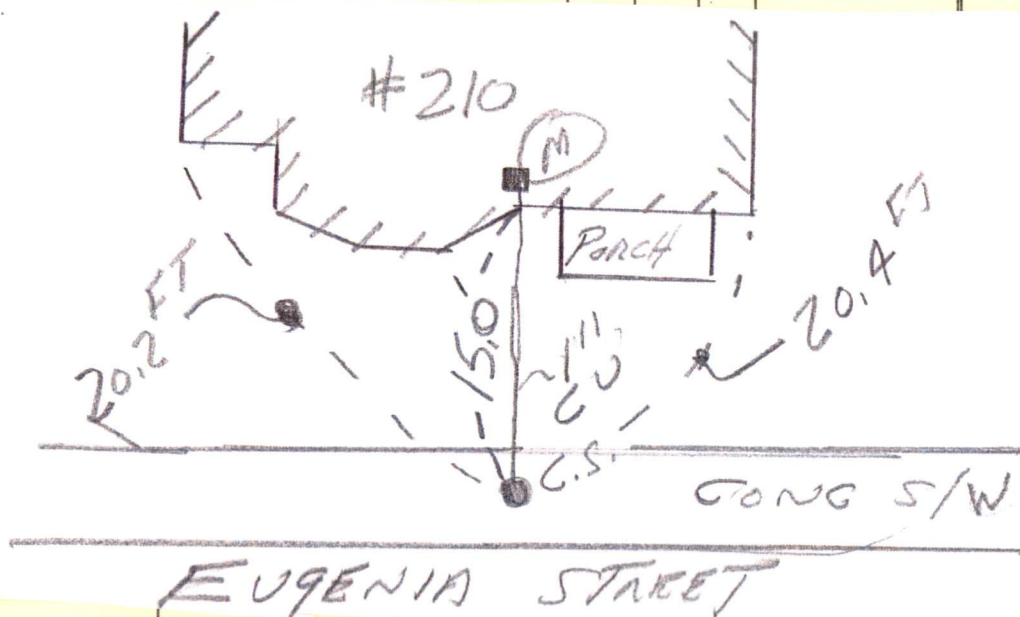

13105

✓

210 Eugenia

OWNER: Florence Sauzon

5/8" L.L.

E from	Ashley Blvd.	94.8
N from S line	Eugenia	9.2
E from W line	House	12.7

Nov. 27, 1961 Renewed from  $\frac{1}{2}$  ft. outside curb stop to  $3\frac{1}{2}$  ft.  
inside curb stop 4 ft. of  $\frac{3}{4}$ " copper tubing  
 $\frac{3}{4}$ " cop. to cop. stop, fig. 415 R.H  
2- lbs. of wiping solder

Sept. 2, 1977: Renewed from main to 1 ft. from main. 1 ft.-3/4" cop.  
3/4" x 3/4" Fig. 413; 3/4" x 5/8" lead to cop. adapt. XS;

Jan 21, 1997: Renewed from main to prop line  
Stock: 16ft 3/4" copper tubing 1-3/4" curb stop  
1- Caldwell stop box 1- 3/4 x 5/8 lead-cop adpat.xs  
1- 3/4 x 5/8 Fig 413\_\_\_\_\_



[illegible]

## CHARGE OUTS

[illegible]
