

APPLICATION No.: 1327

TAP CLEARED

LOCATION: 1594 - 1598 Purchase St

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: 1" Copper Service

07/10/2019 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Water pressure 90 Diameter 1in

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 33

Distance from curb face to curb stop (ft) 3

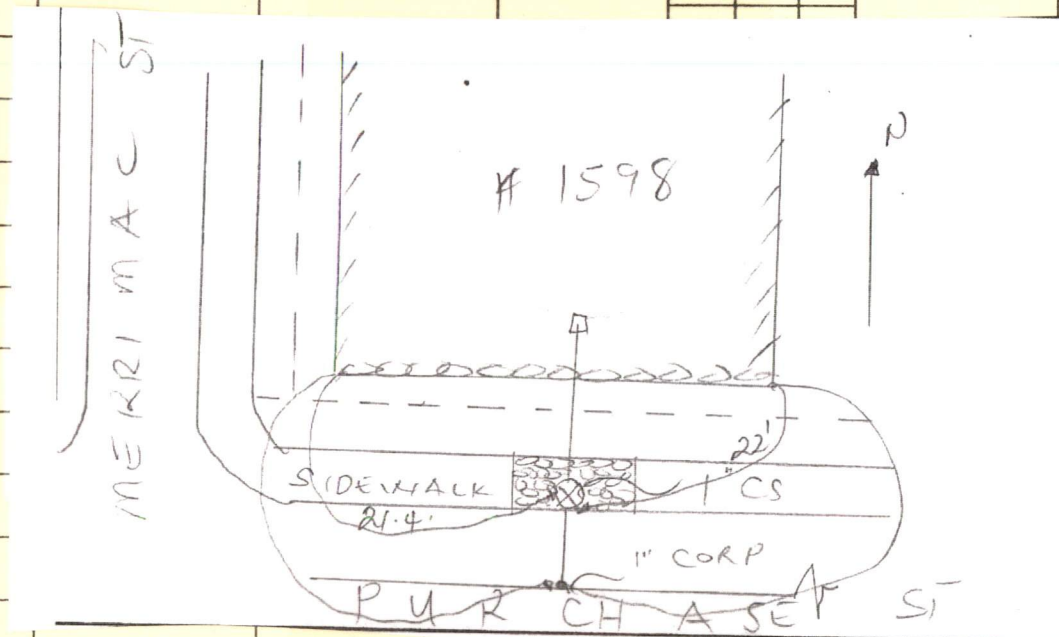
Depth of service (ft) 4

Total length of new pipe installed (ft) 33

Curb stop replaced: NO size N/A

Corporation replaced: No

Ball valve replaced: Yes size 1"

[illegible]

APPLICATION No.: 1327

TAP CLEARED

LOCATION: 1594-1598 PurchaseOWNER: LipsittMEASURES: 5/8"S from E Merrimac22.4W from E line Purchase~~8.2~~ 7.7 ft.N from S line house3.2S x N line bldg.22.0 ft.

July 23, 1982 Renewed from the main to $1\frac{1}{2}$ ft. inside
curb stop

30 ft. - $\frac{3}{4}$ " Copper tubing $\frac{3}{4}$ " Curb stop

1 Caldwell Stop Box $\frac{3}{4}$ " x $\frac{5}{8}$ " Fig. 413

Tap reamed $\frac{3}{4}$ " x $\frac{5}{8}$ " lead to copper
adaptor XXS

- - -

Oct. 5, 1983 Renewed from curb stop to the property line.

PURCHASE ST. WIDENING

7 ft. - $\frac{3}{4}$ " copper tubing Caldwell stop box

$\frac{3}{4}$ " curb stop $\frac{5}{8}$ " x $\frac{3}{4}$ " lead to cop adapt XS

DATE

BEF.

AFT.

REMARKS



[illegible]

CHARGE OUTS

[illegible]
