

APPLICATION No.: 13345

## TAP CLEARED

LOCATION: 66 - 68 Cove St

OWNER: \

31-313

MEASURES: 4/30/2019

1" Copper Service

Lead Service Line Replacement Program, Phase 1

Contractor P. Gioioso &amp; Son

Type CU, Diameter(in) 1, Water pressure 100

Distance from main to curb stop (ft) 27

Distance from curb stop to meter (ft) N/A

Distance from curb face to curb stop (ft) 1.8

Depth of service (ft) 4.5

Total length of new pipe installed (ft) 27

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

Ball Valve furnished: no

DATE

BEF.


AFT.

REMARKS

# METER HISTORY

## CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

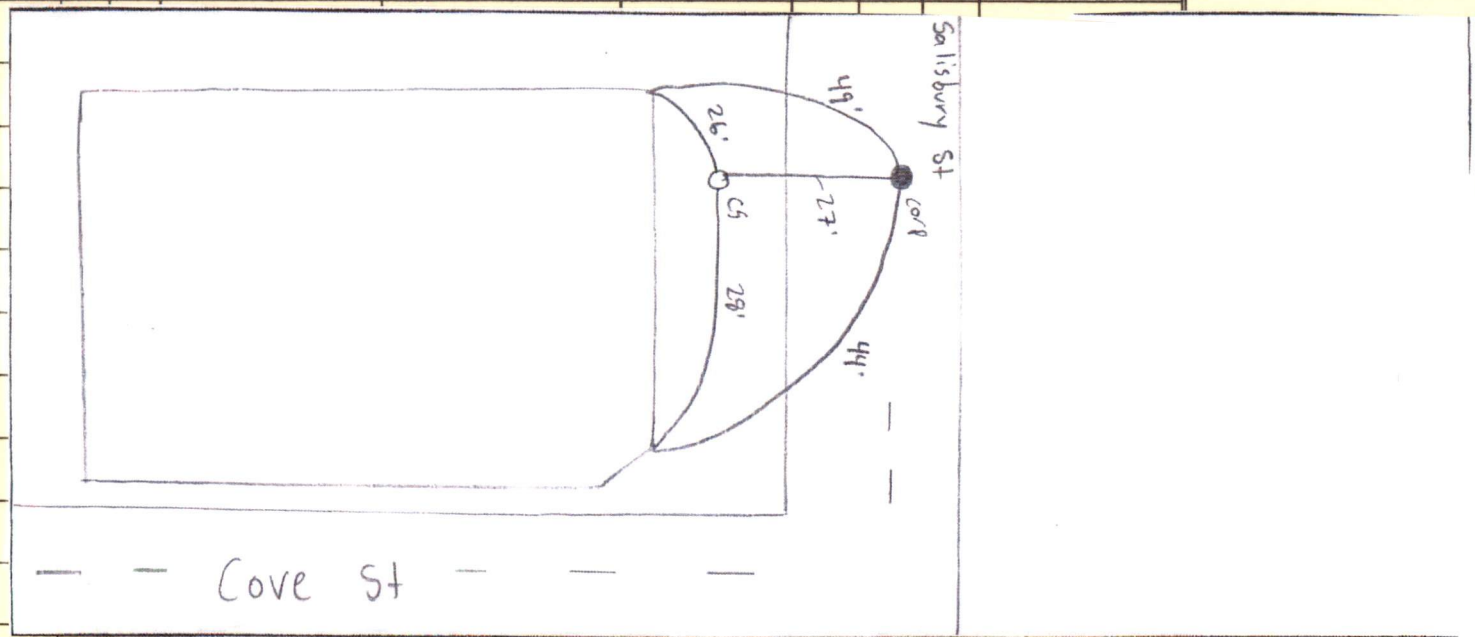

APPLICATION No.: 12345TAP CLEARED 86 23-1139LOCATION: 66-68 Cove St.OWNER: Walter Kocor Et UxMEASURES: 5/8" H lead May 5, 1910

S from Cove St. 36.5 ft.

W from E line Salisbury St. 8.0 ft.

N from S line bldg. 21.0 ft.

6/10/86: Renewed from 1/2' outside curb stop to ins. cellar.

( 2 ft. ins. prop line) Stock: 11ft. - 3/4" copper tubing

1 - 3/4" curb stop 1 - Caldwell stop box 1 - 3/4 x 5/8 lead to  
cop adapt. xxs.*Maint - 1/2' extra**68 Cove St**25063*

DATE

BEF.

AFT.

REMARKS



[illegible]

## CHARGE OUTS

[illegible]
