

APPLICATION No.: 13822

TAP CLEARED

LOCATION: 49 Fair St

OWNER: _____

31-313

MEASURES: 1" Copper Service

09/19/2018 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) N/A

Distance curb stop to meter (ft) 21

Distance from curb face to curb stop (ft) 1.5

Depth of service (ft) 4.7

Total length of new pipe installed (ft) 21

Curb stop replaced: no

Corporation replaced: no

Ball valve furnished: yes, size 1"

DATE

BEF.


AFT.


REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST	REMARKS

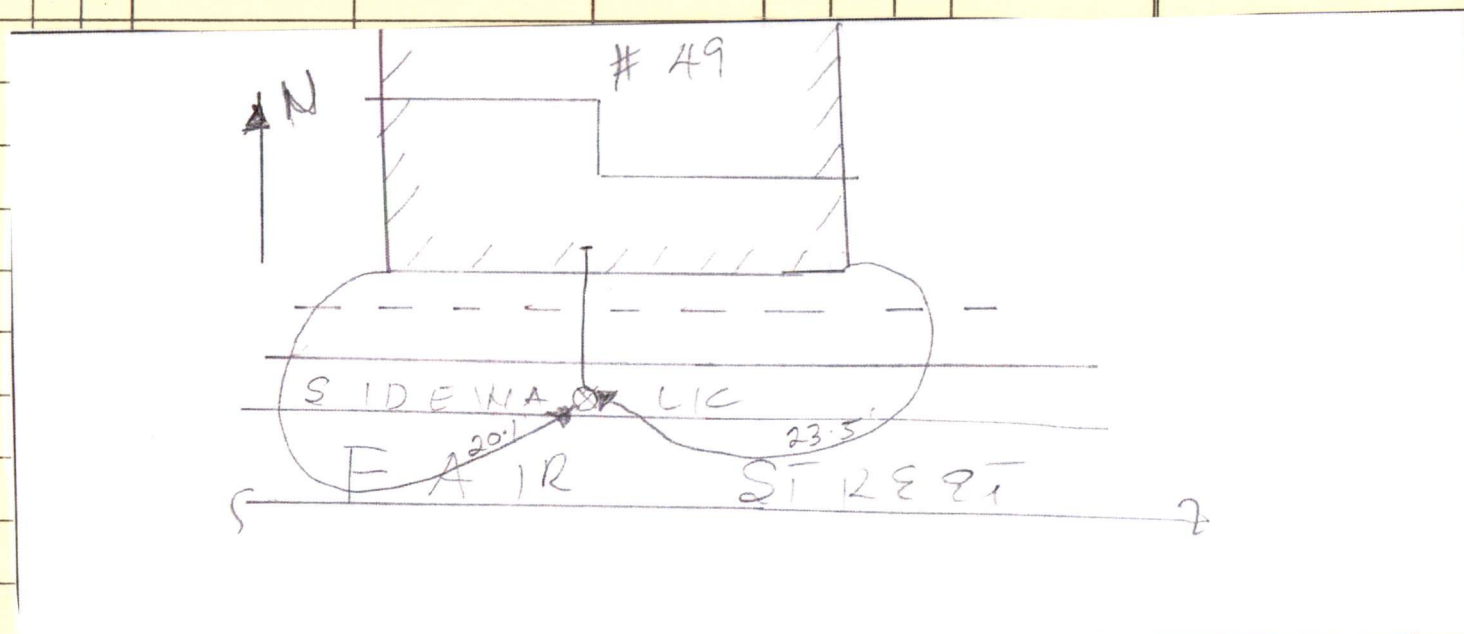

APPLICATION No.: 13822TAP CLEARED LOCATION: 49 Fair St.OWNER: Mannuel C. Tavares

DATE

BEF.

AFT.

REMARKS

9/8/77

Tap reamed

MEASURES: 5/8" H lead Nov.10,1910

E from W line Hall St. 10.4 ft.

S from N line Fair St. 8.8 ft.

E from W line house 10.3 ft.

Jan. 16, 1964 Renewed from 6" outside curb stop to
2 ft. inside curb stop

2 1/2 ft. 3/4" copper tubing

1 3/4" cop. to cop. stop. fig 415

2 side walk out 4' x 4' cement

Ingersoll -Rand compressor: 1 hr.

Abraham

Fields

Whelan

Sept. 8, 1977: Replaced lead from main to 18 ft. front of main.

Manhole installed & copper goes around west side of manhole.

Hole will be mainted by Warren Bros. who installed manhole.

18 ft.-3/4" copper; 3/4" x 3/4" lead to cop. adapt. XXS;

3/4" x 3/4" Fig. 413;

12/12/06 Renewed from 18 ft. from main to property line.

Stock: 18 ft/ 3/4" copper tubing; 3/4" curb stop; Caldwell

stop box; 5/8" x 3/4" lead-cop adapt. XS; 3/4" x 3/4"

cop=cop cplg., comp;

Also replaced 7 ft. 6" PVC sewer pipe service Stock:

7 ft. 6" PVC pipe; 2 rub cplgs. clay-PVC Bento

[illegible]

CHARGE OUTS.

[illegible]
