

APPLICATION No.: 14003

TAP CLEARED

LOCATION: 204 - 206 Eugenia St

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: 1" Copper Service

04/04/2018 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 59

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 31.0

Distance from curb face to curb stop (ft) 1.0

Depth of service (ft) 3.2

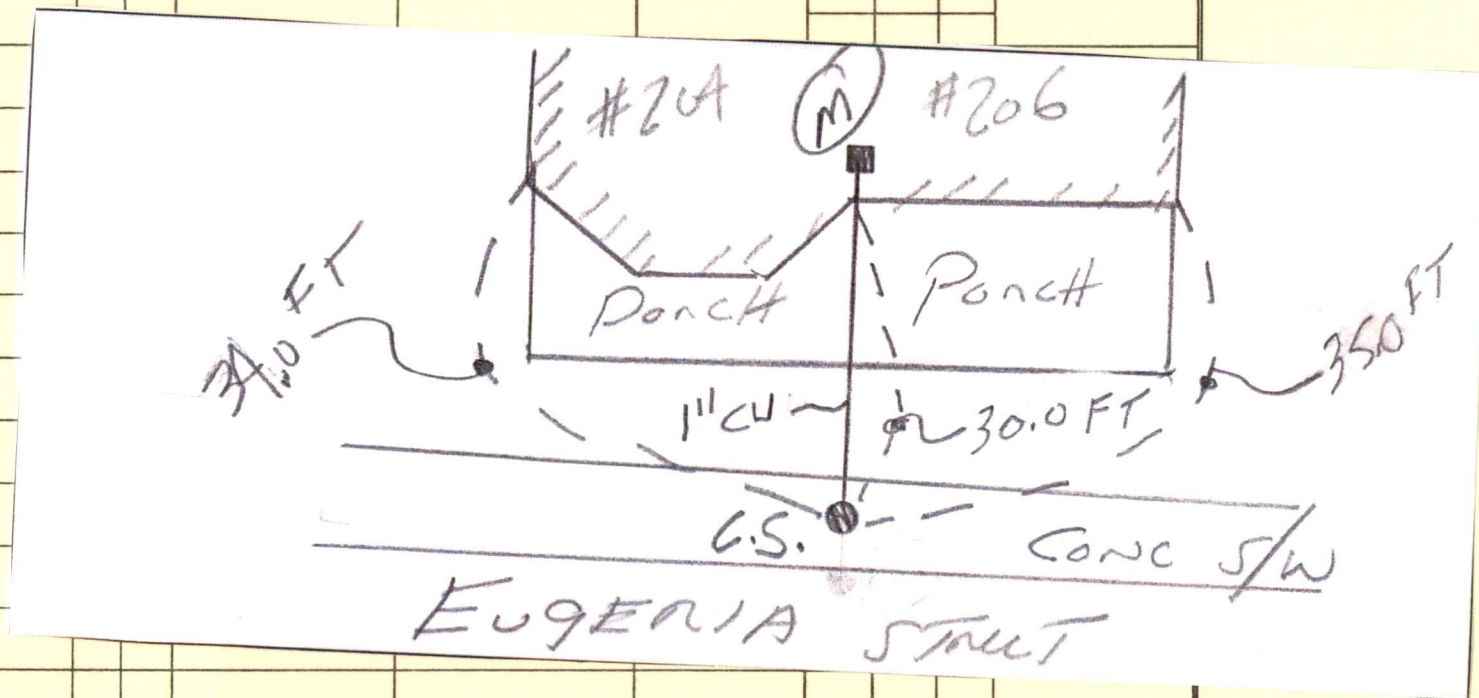
Total length of new pipe installed (ft) 34.0

Curb stop replaced: no

Corporation replaced: no

Ball valve furnished: yes, size 1"

Remarks: 30.0 curb stop to house, 1.0 wall thick-
ness to meter, 3.0 WHIP

[illegible]

14003

TAP CLEARED 8239-1664

LOCATION: 204-206 Eugenia

OWNER: ~~Frank Jeglenski~~

MEASURES: $5/8''$

| | | |
|---------------|--------------|-------|
| E from | Ashley Blvd. | 179.0 |
| N from S line | Eugenia | 9.5 |
| W from E line | House | 14.1 |

Nov. 23, 1976 Renewed from ½ ft. outside curb stop to the prop. line.

8 ft. - 3/4" Copper tubing 3/4" Curb Stop
Caldwell Stop Box 2 - 5/8" x 3/4" lead to cop.

OCT 1 1982 -- Renewed from main to a point 3.3 ft. from main. 3.3 ft.-3/4" copper; 5/8" x 3/4" Fig. 413; 3/4" x 5/8" lead-cop. adapt. XS;

| DATE | B.E.F. | A.F.T. | REMARKS |
|------|--------|--------|---------|
|------|--------|--------|---------|

OCT 1

BEF.

AFT.

REMARKS

Reamed

[illegible]

CHARGE OUTS

[illegible]

33513 - FS

APPLICATION No.:

LOCATION:

204 - 206 Eugenia St

OWNER:

Silvino Carreiro

Contractor: Dennis Trucking

31-313

MEASURES:

2" Copper - Fire Supply 04-21-2009

| | |
|---------------------------|-------|
| E from E line Ashley Blvd | 189.0 |
| N from S line Eugenia St | 8.0 |
| E from W line House | 25.0 |
| W from E line House | 5.5 |
| N from N line House | 29.0 |
| Main to Property line | 18.0 |
| Pipe inside property | 20.0 |

TAP CLEARED

DATE

BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

[illegible]
