

APPLICATION No.: 14020

LOCATION: 143 - 145 Fair St

TAP CLEARED

DATE \_\_\_\_\_

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: April 10, 1911

N X Fair St 32.9 ft

E X W line Sears St 6.3 ft

N X N line House 23.4 ft

1" Copper Service

10/02/2018 Lead Service Line Replacement Program

Phase 1, Contactor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) 24

Distance curb stop to meter (ft) 19

Distance from curb face to curb stop (ft) 1.5

Depth of service (Ft) 4.5

Total length of new pipe installed (ft) 43

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

Ball valve furnished: yes size 1"

143 Fair St

Date: 9/22/2016

Contractor: Riley Brothers

Service Hit, repaired by DPI

Cop- ¾ Box of Copper Tubing Units 3 UOM Feet


LCXXS – 5/ 5/8" to 3/4" Lead to Copper 8 x 3/4 coupling XXS Units 2 UOM Each

CSValve – 3/4" Curb Stop Valve 3/4 Units 1 UOM Each

# METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

## CHARGE OUTS

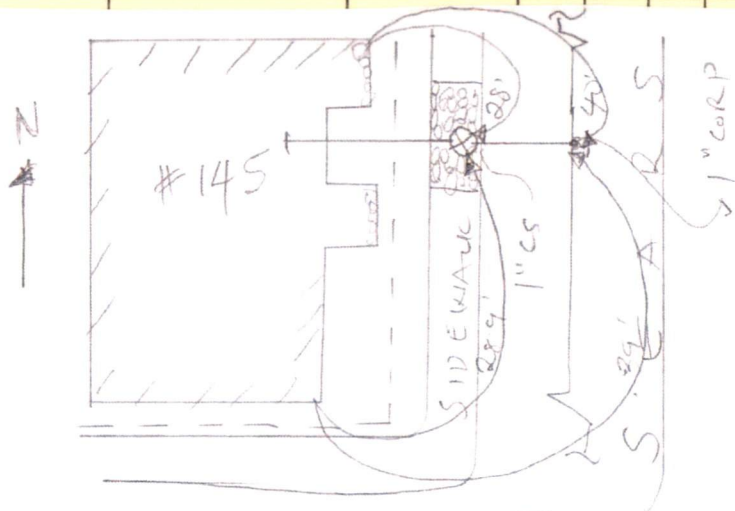

FAIR ST
