

APPLICATION No.: 14886

LOCATION:

119 CLIFFORD ST.

OWNER:

S. Lafrance

31-313

TAP CLEARED

DATE

BEF.

AFT.

REMARKS

Measures:	5/8"	L	08.23.1912
	E from	Arlington	101.7'
	S x N line	Clifford	8.5'
	W x E line	House	9.6'
	E x W line	House	17.4'
	S x S line	House	14.3
	Main to Property line		34'
	Pipe inside Property		7'

1" Copper Service

09/08/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 24'

Distance from curb stop to meter 12.5'

Distance curb face to curb stop 2'

Depth of Service 4'

Total length of new pipe installed 36.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"


Ball Valve replaced yes N/A

Remarks: Type C-1" Copper to meter 0' Lead pipe removed.

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

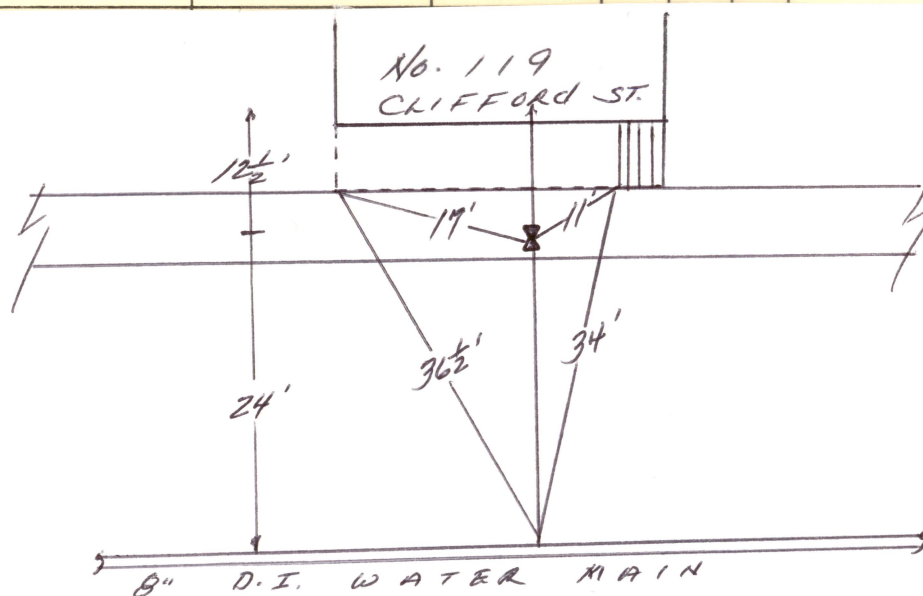

CLIFFORD ST.
