

APPLICATION No.:

LOCATION:

OWNER:

Measures:	5/8"	L Lead	08.26.1912
	E from	Concord	99.4'
	N from S line	Clifford	9'
	W from E line	House	14'

08/24/2022 2022 Water main improvement program

Type CU Diameter 1"

Distance from main to curb 10.5'

Distance from curb stop to meter 14'

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 24.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes 1"

Remarks: Type C -1" Copper to meter, 8' Lead removed.


DATE _____

BEF.

AFT.

REMARKS

METER HISTORY							
DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST	REMARKS

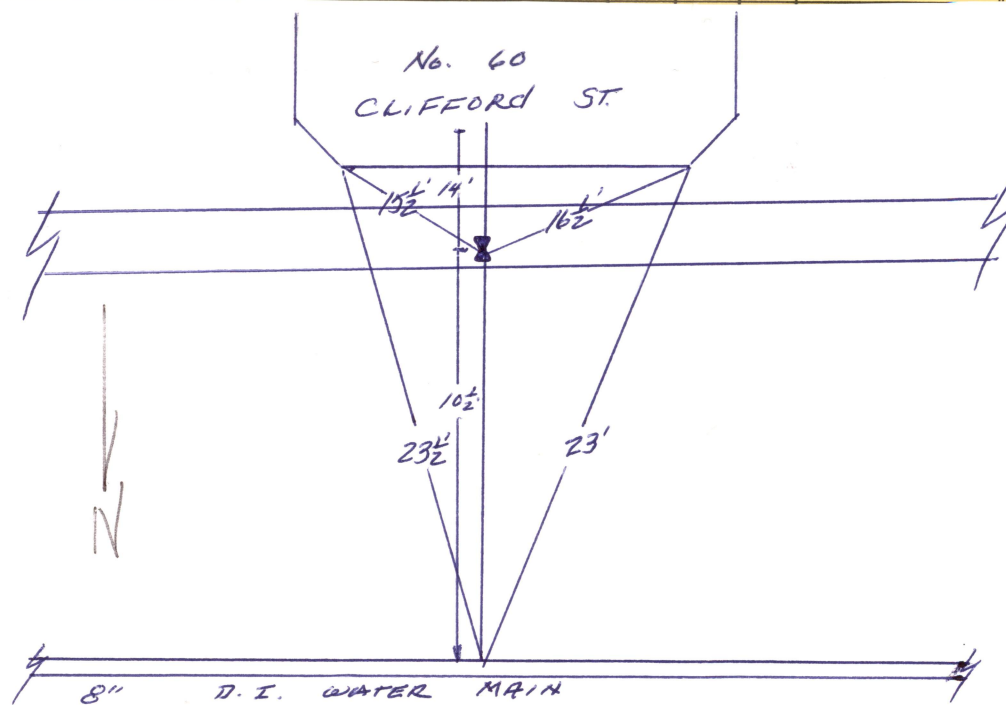

C L I F F O R D S T.

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: CLIFFORD ST.

HOUSE No: 60

Contractor: C. Naughton Corp.

Date: 8-24-22

Type: CU Diameter (in): 1

Distance from main to curb stop (ft): 10 1/2'

Distance curb stop to meter (ft): 14'

Distance from curb face to curb stop (ft): 1.5'

Depth of Service (ft): 4.5'


Total length of new pipe installed (ft): 24.5'

Curb Stop Replaced: Yes Size (in): 1

Corporation Replaced: Yes Size (in): 1

Ball Valve Replaced: Size (in): 1

Ties:

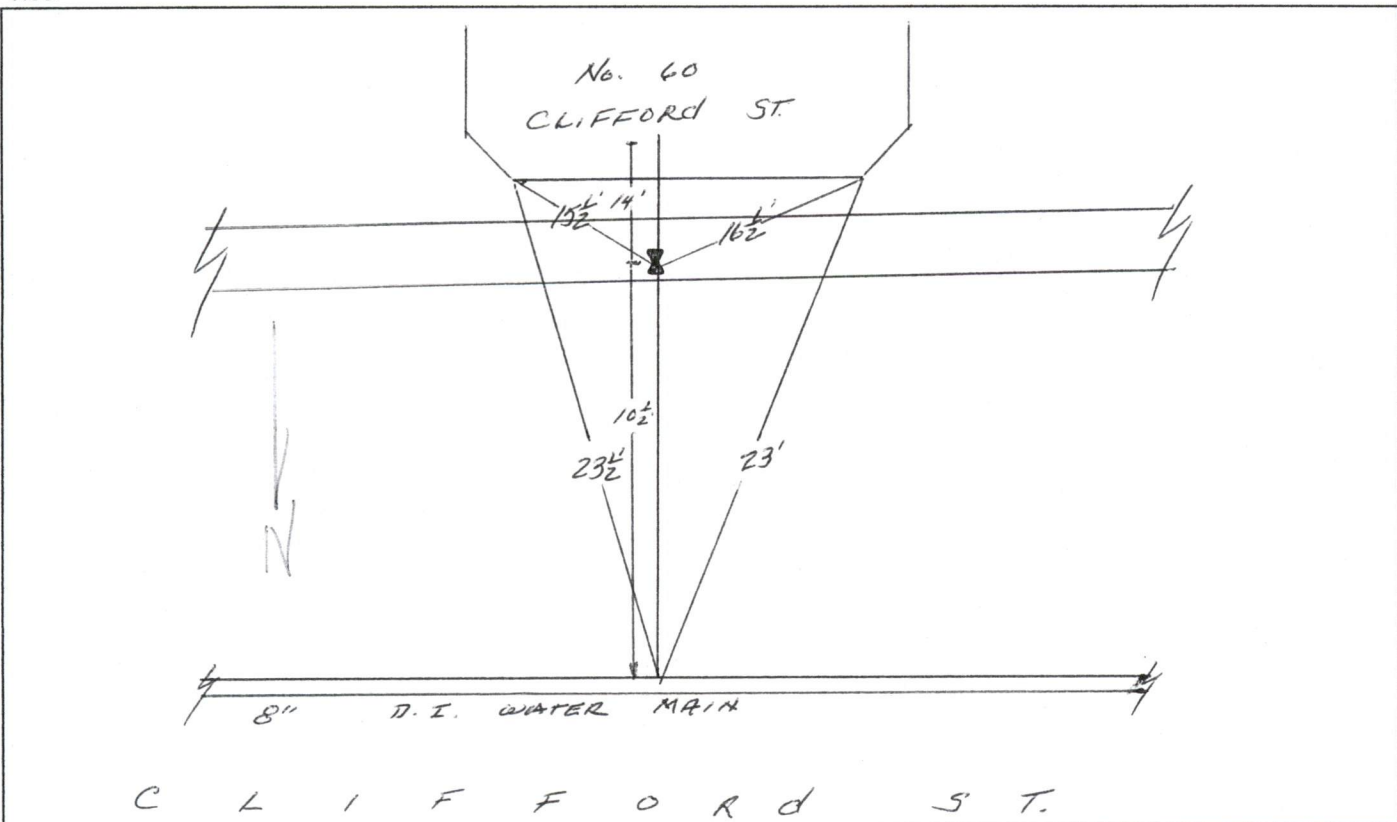

Remarks:

TYPE C - 1" COPPER TO METER, 8' LEAD REMOVED
