

✓ APPLICATION No.: 15248

LOCATION: 252 Whitman St

OWNER:

31-313

MEASURES:	W X Ashley Blvd	310.7 ft
	N X S Whitman St	9.2 ft
	E X W House	15.6 ft

1" Copper Service 4/23/2018
Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 65
Distance from main to curb stop (ft) N/A
Distance from curb stop to meter (Ft) 18
Distance from curb face to curb stop (ft) 1.3
Depth of service (Ft) 3.7
Total length of new pipe installed (ft) 21
Curb stop replaced: No
Corporation replaced: No
Ball Valve replaced: Yes size 1"
Remarks: 3ft whip

TAP CLEARED

DATE _____

BEF.

AFT.


REMARKS

11/23/2004 Ream

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

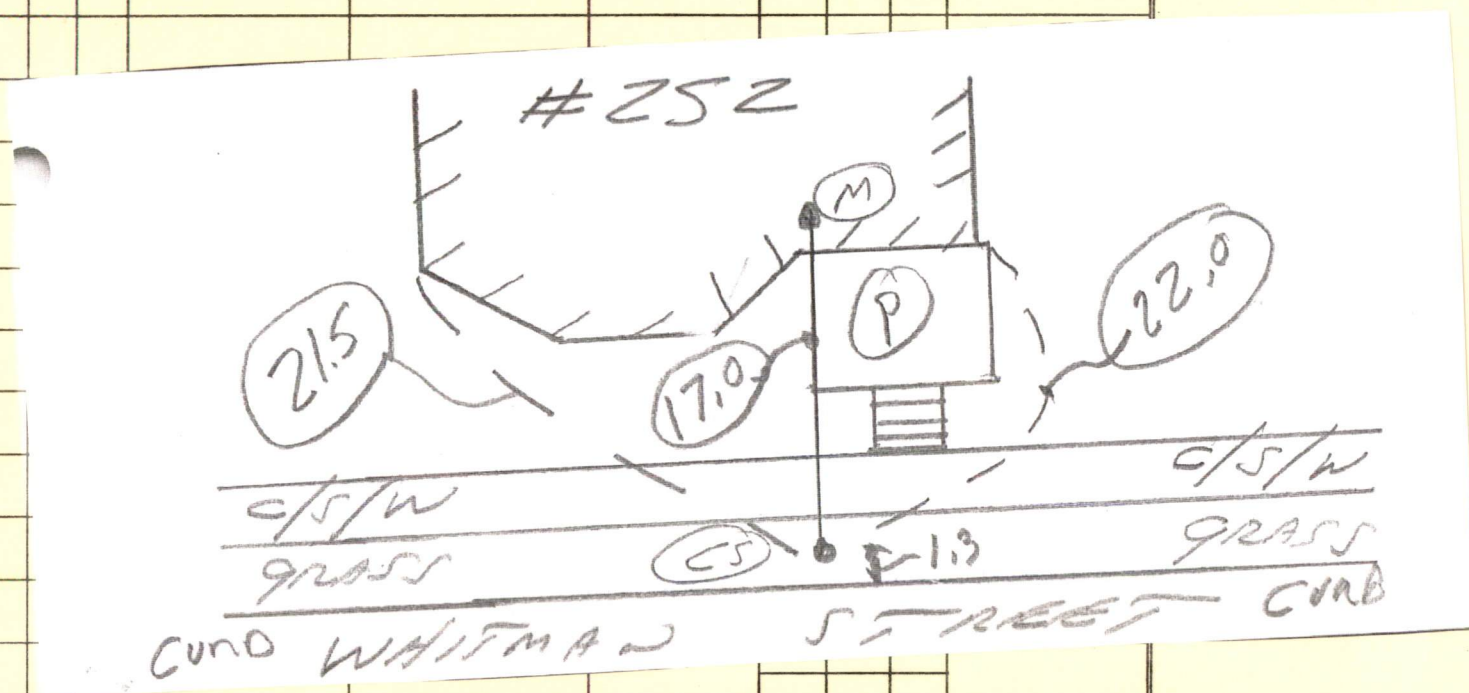

APPLICATION No.: 15248

TAP CLEARED

8412-0707

LOCATION: 252 Whitman S.S.W. of Bowditch

OWNER: Victora Charles

MEASURES: 5/8"

W from	Ashly Blvd.	310.7 ft.
N from S	Whitman	9.2 ft.
E from W	house	15.6 ft.

Jan. 5, 1953 Renewed from the curb stop to 2 ft. to a point in
the sidewalk.
2 ft. of 3/4" copper tubing

March 20, 1984 - Renewed from 1 ft. outside curb stop
to a point 6 ft. inside curb stop.
7 ft. - 3/4" copper tubing
1 - 3/4" curb stop 1 stop box
2 - 5/8" x 3/4" lead to copper adaptors XS

11/23/04 Renewed from main to curb stop. Stock: 12 ft. 3/4" copper
tubing; 3/4" curb stop; Caldwell stopbox; 5/8" x 3/4" Fig. 413
Tap reamed

DATE

BEF.

AFT.

REMARKS

4/23/04 8:30 AM 2004-480-2285
11/23/04 Tap reamed

[illegible]

This image shows a blank, aged, cream-colored page, likely an endpaper or flyleaf of a book. The paper has a slightly textured appearance with some faint horizontal lines and small dark spots, possibly due to age or handling. The page is set against a dark background.
