

APPLICATION No.: 15413

TAP CLEARED

B 2058

LOCATION: 560 Allen St.

OWNER: Joaquim Moniz, Et Ux

DATE

BEF.

AFT.

REMARKS

3/27/90: TAP REAMED

MEASURES: 5/8" L ~~lead~~ COPPER Oct. 2, 1913

E from Reed St. 71.0 ft.

N from S line Allen St. 7.0 ft.

W from E line house 2.8 ft.Feb. 17, 1981: Renewed from 6" outside ^{CH} to the property line.
6.0 ft. - 3/4" copper

1-3/4" curb stop 1-Caldwell stop box

2-5/8" x 3/4" lead-cop. adapt. XS

3/27/90: Renewed from main to curb stop.
Stock: 9ft. - 3/4" copper tubing same curb stop
same Caldwell stop box 1-3/4x5/8 Fig. 413CHAP 90 PROJ.5/30/2019: Lead service line replacement program phase 1
Contractor: F. Gioioso & sons. Inc

Type: CU, Diameter 1, Water Pressure 60

Distance from main to Curb stop N/A

Distance curb stop to meter 15'

Distance from curb face to curb stop 2'

Depth of service 4'

Total Length of new pipe installed 15'

next card →

METER HISTORY

CHARGE OUTS

[illegible]

15413

APPLICATION No.:

TAP CLEARED

LOCATION: 560 Allen St

DATE

BEF.


AFT.

REMARKS

OWNER:

31-313

MEASURES: Curb stop replaced NO: Size N/A
 Corporation replaced NO: Size N/A
 Ball Valve furnished YES: Size N/A

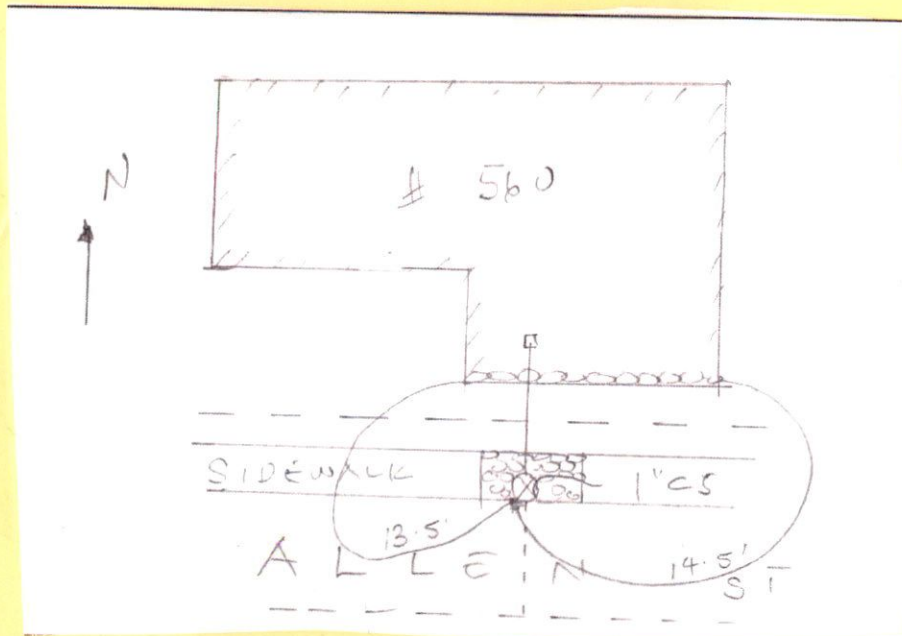

METER HISTORY

CHARGE OUTS

[illegible]
