

APPLICATION No.: 15449

LOCATION: 122 CLIFFORD ST.

OWNER: Alexander Phaneuf

31-313

Measures:	5/8"	H Lead	10.31.1913
	E from	Arlington	66.8'
	N from S line	Clifford	8.4'
	W from E line	House	11.2'

1" Copper Service

09/07/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 10'

Distance from curb stop to meter 21.5'

Distance curb face to curb stop 2'

Depth of Service 4'

Total length of new pipe installed 31.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes N/A

Remarks: Type C-1" Copper to meter 20' Lead pipe removed.

TAP CLEARED

DATE _____

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

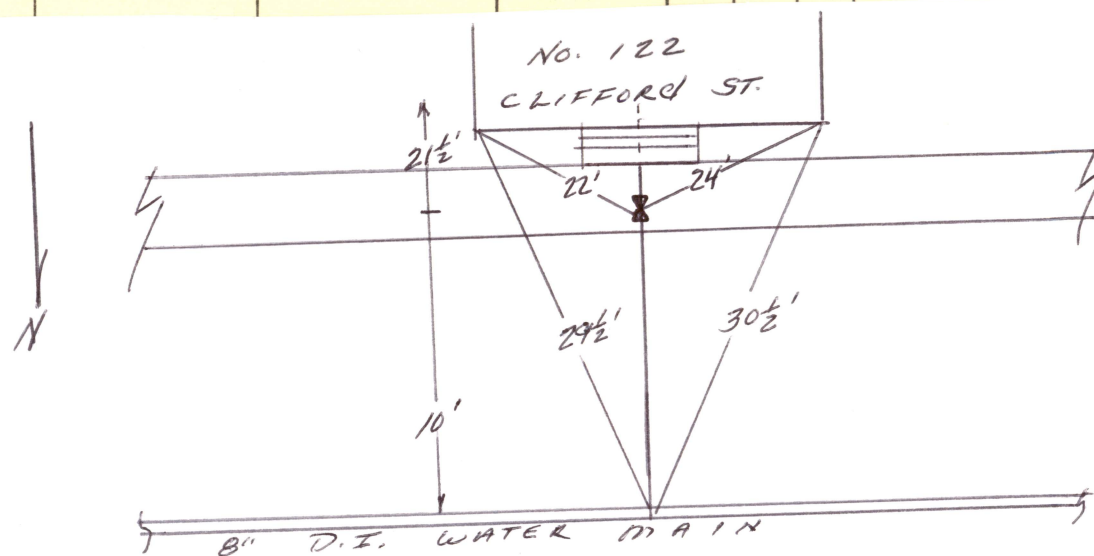

CLIFFORD ST.
