

APPLICATION No.: 15872

LOCATION: V 209 - 211 Nash Rd

TAP CLEARED

OWNER: 31-313

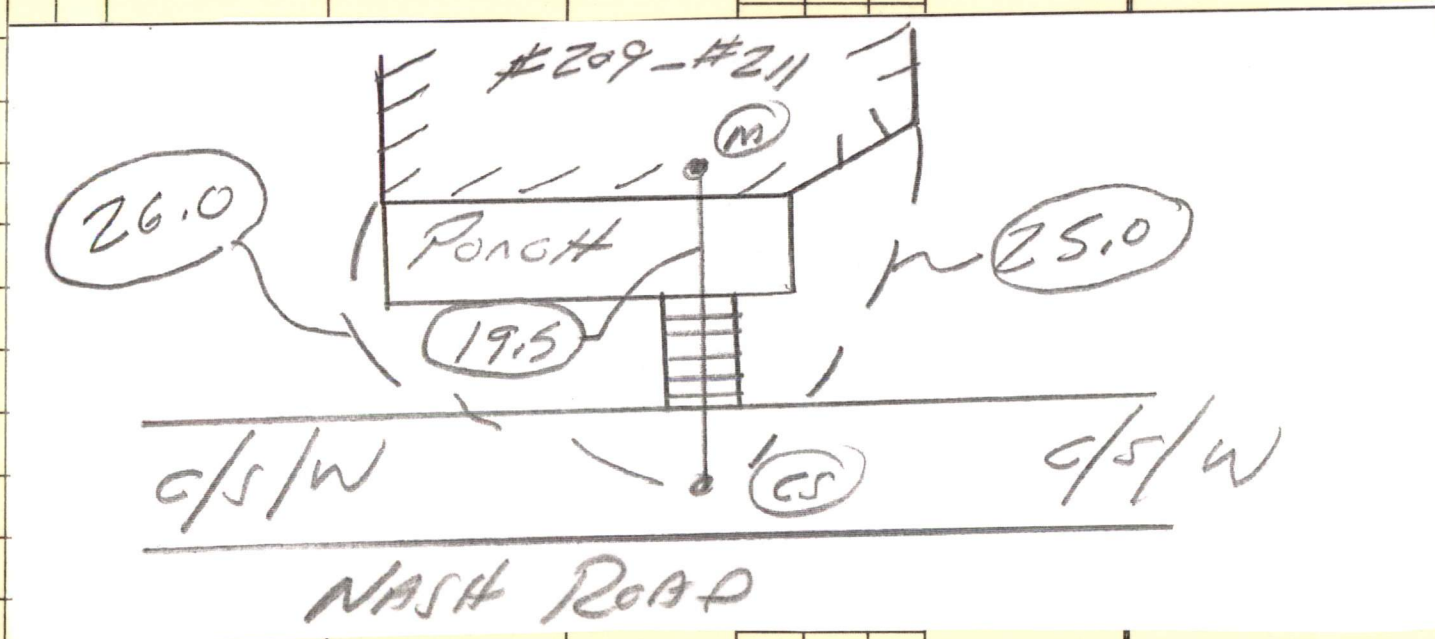
MEASURES: 1" Copper Service
05/24/2018 Lead Service Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Water Pressure 65 Diameter 1in
Distance from main to curb stop (ft) N/A
Distance curb stop to meter (ft) 20.5
Distance from curb face to curb stop (ft) 2.0
Depth of service (ft) 4.3
Total length of new pipe installed (ft) 23.5
Curb stop replaced: No
Corporation replaced: No
Ball valve replaced: Yes size 1"
Remark: 3.0 WHIP

DATE

BEF.

AFT.

REMARKS

[illegible]

APPLICATION No.: 15872

TAP CLEARED

LOCATION: 209 Nash Rd. N.S. E. of Ashley Blvd.

OWNER: Daniel A. Fortin

MEASURES: 5/8"
E from Ashley Blvd. 173.0 ft.
S from N line Nash Rd. 9.0 ft.
E from W line House 17.3 ft.

DATE

BEF.

AFT.

REMARKS

9-21-98 Tap reamed

Dec. 3, 1959 Renewed from curb stop to 3 ft. inside
curb stop.

3 ft. - 3/4" Copper tubing 2# wiping solder
- - -

Nov. 15, 1976 Renewed from 6" outside curb stop to the
property line.

12 ft. - 3/4" Copper tubing 3/4" Curb Stop

2 - 5/8" x 3/4" lead to cop. adaptor XS
- - -

9-21-98 - Renewed from main to curb stop. Stock: 35 ft.

3/4" Copper tubing, 1 - Caldwell Stop Box, 1 - 5/8" x 3/4"

Fig. 413. D.W. White to maintain trench.

[illegible]

CHARGE OUTS

[illegible]
