

APPLICATION No.: 15935

TAP CLEARED 89323765

LOCATION: 250 Tinkham

OWNER: Mary Amaral

MEASURES: 5/8"

W from- Ashley Blvd. 196.0 ft.

N from S line Tinkham 8.0 ft.

E from W line house 2.3 ft.

8/10/89: Renewed from main to prop line. Stock: 20 ft. 3/4"

copper tubing 1-3/4" curb stop 1-Caldwell stop box

1 - 3/4x5/8 lead to cop adapt. xs 1-3/4x5/8 Fig. 413

05/25/2018 1" Copper Service

Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 70

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (ft) 17.5

Distance from curb face to curb stop (ft) 3

Depth of service (ft) 3.5

Total length of new pipe installed (ft) 20.5

Curb stop replaced: No, Corporation replaced: No

Ball valve furnished: Yes size 1"

DATE

BEF.

AFT.


REMARKS

8/10/89: TAP REAMED

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS
12/22/43		5/8	Hersey D.	533391					

CHARGE OUTS

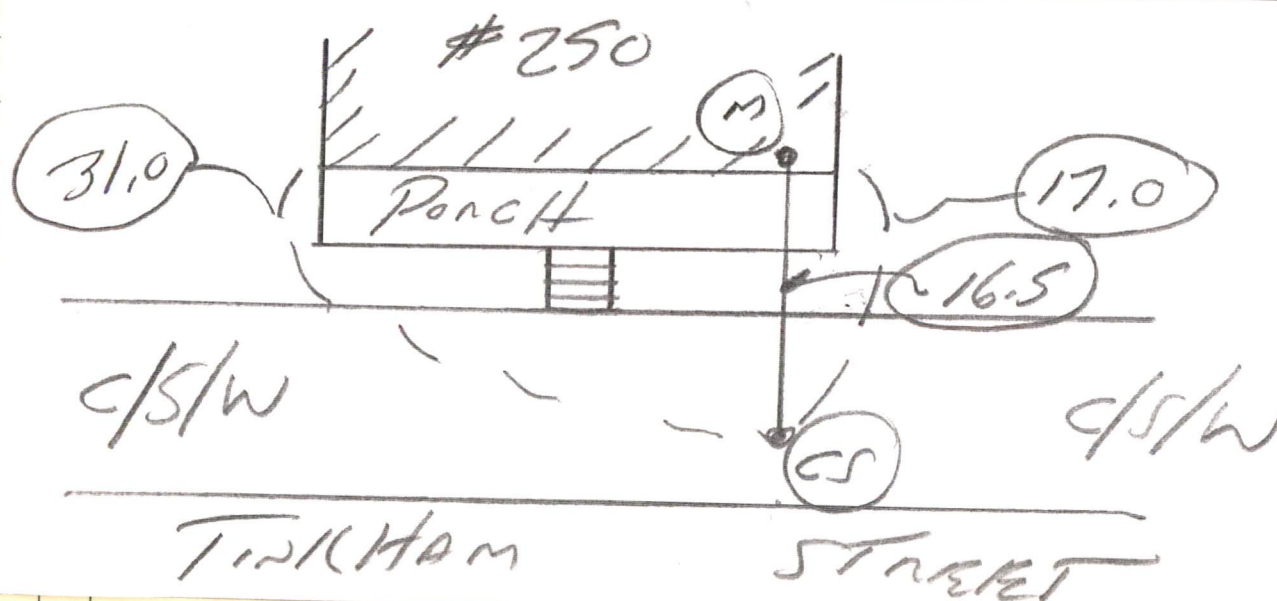

APPLICATION No.: 15936 C

·LOCATION: Rear S. side 250 Tinkham

OWNER:

MEASURES: 5/8"

Connection of Ser. # 15935

TAP CLEARED

[illegible]

[illegible]

CHARGE OUTS

[illegible]
