

APPLICATION No.: 15989

LOCATION: 2 PRISCILLA St.

OWNER: Vicent Peternele

31-313

Measures:	5/8"	L Lead	10.20.1914
	S from	Priscilla St	27'
	E from W line	West St	9'
	N from S line	house	14'

1" Copper Service

08/04/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 30'

Distance from curb stop to meter 10'

Distance curb face to curb stop 1.5'

Depth of Service 4'

Total length of new pipe installed 40'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes 1"

Remarks: 10' Lead replacement Type C-1" Copper to meter


TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

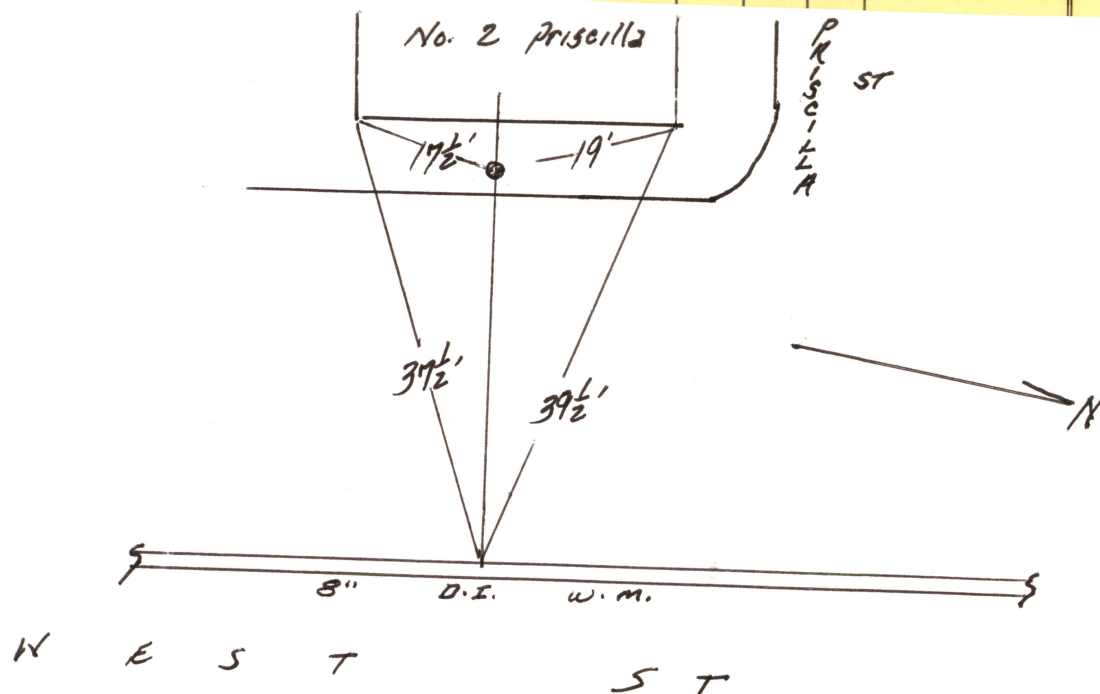[illegible]

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: PRISCILLA

HOUSE No: 2 PRISCILLA ST.

Contractor: C. Naughton Corp.

Date: AUG 4, 2022

Type: CU Diameter (in): 1

Distance from main to curb stop (ft): 30'

Distance curb stop to meter (ft): 10'

Distance from curb face to curb stop (ft): 1.5

Depth of Service (ft): 4


Total length of new pipe installed (ft): 40

Curb Stop Replaced: Yes Size (in): 1

Corporation Replaced: Yes Size (in): 1

Ball Valve Replaced: Size (in): 1

Ties:

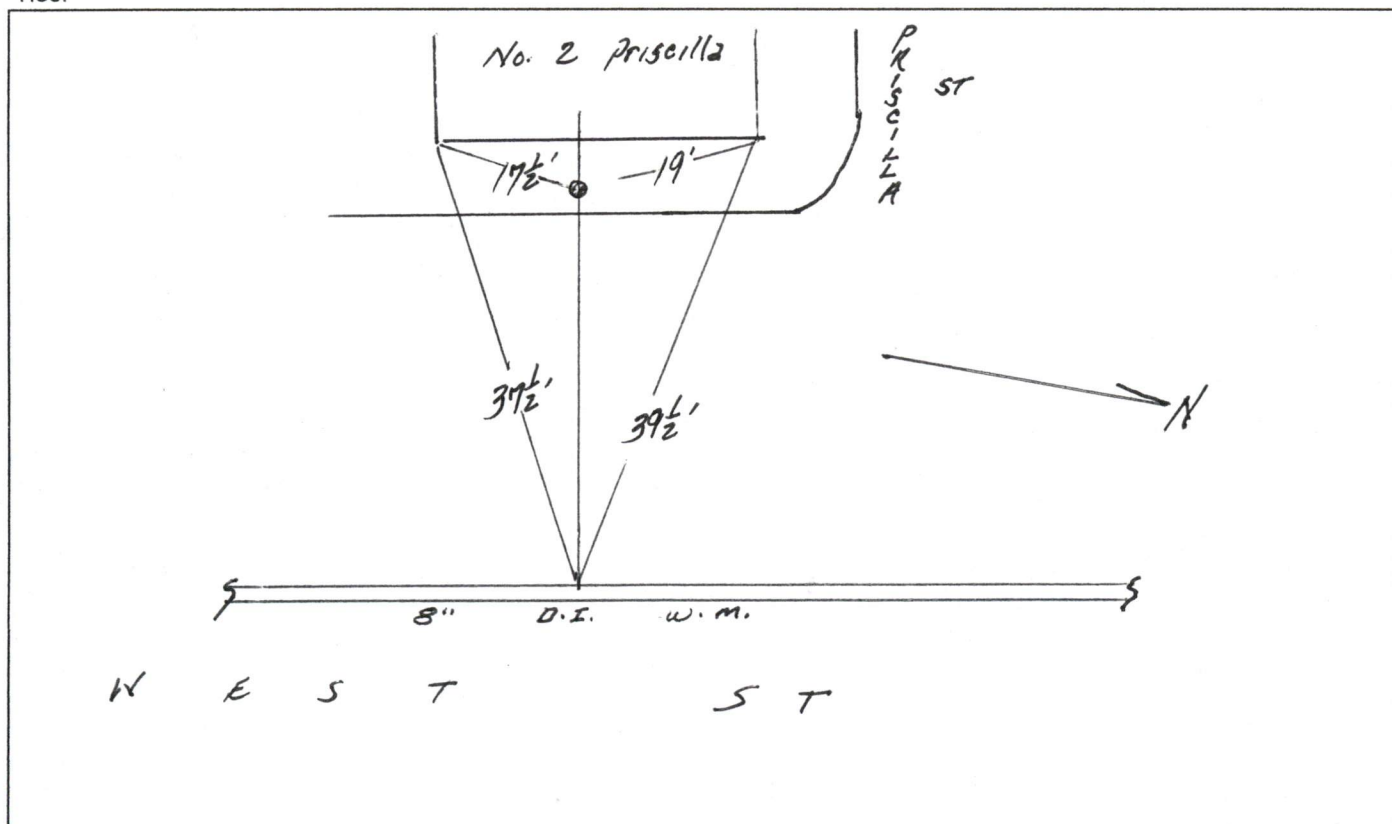

Remarks:

10' LEAD REPLACEMENT
TYPE C - 1" COPPER TO METER
