

APPLICATION No.: 16010

LOCATION: 71 WEST ST.

OWNER: Jos T. Baldwin
31-313

Measures:	5/8"		
	S from	Taber	57.5'
	E from W	West	8.5'
	N from S	house	4'

1" Copper Service

08/08/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 26'

Distance from curb stop to meter 22'

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 48'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes 1"

Remarks: 22' $\frac{3}{4}$ "Lead Service Removed Type C-1" Copper to meter

TAP CLEARED

DATE _____

BEF.


AFT.

REMARKS

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

CHARGE OUTS

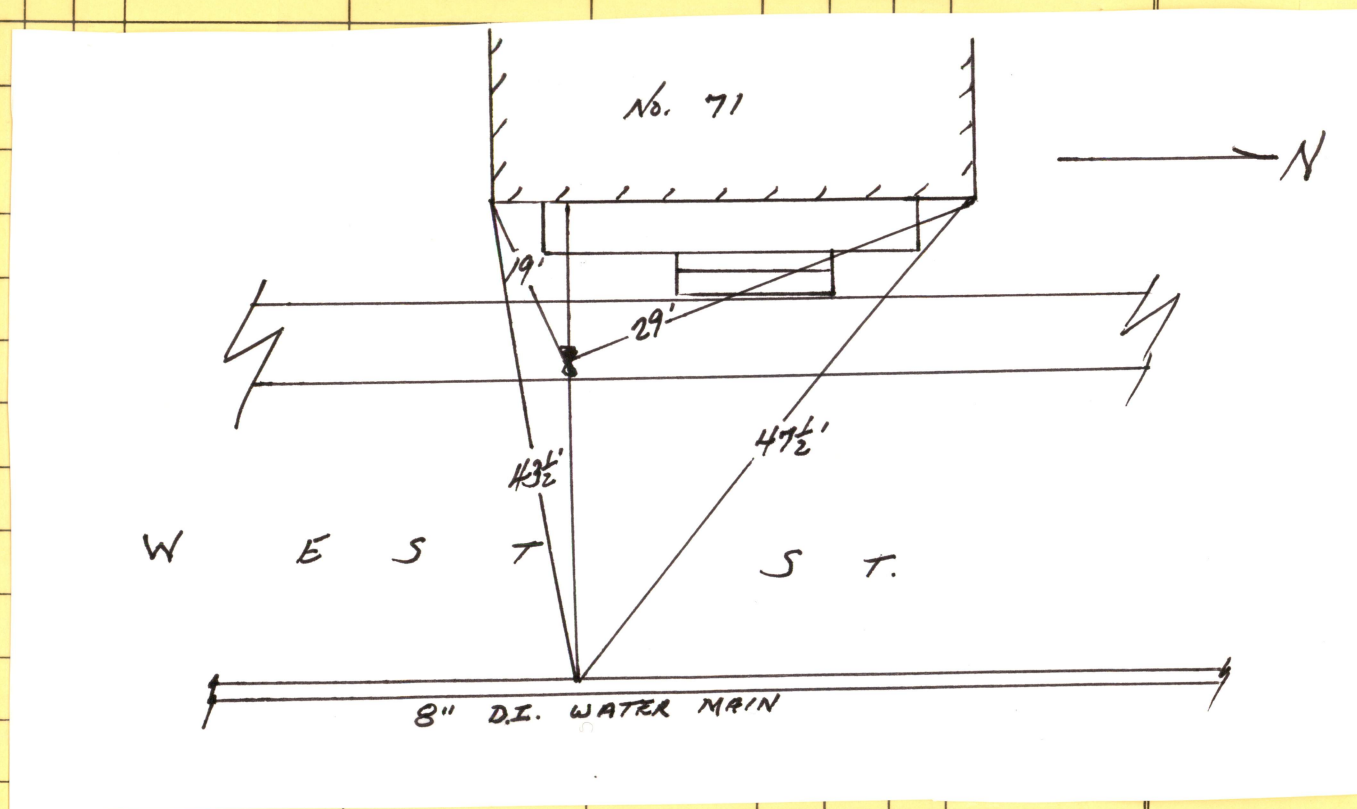

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: WEST ST.

HOUSE No: 71

Contractor: C. Naughton Corp.

Date: 8-8-22

Type: CU Diameter (in): 1

Distance from main to curb stop (ft): 26'

Distance curb stop to meter (ft): 22'

Distance from curb face to curb stop (ft): 1.5'

Depth of Service (ft): 4.5'


Total length of new pipe installed (ft): 48'

Curb Stop Replaced: Yes Size (in): 1

Corporation Replaced: Yes Size (in): 1

Ball Valve Replaced: Size (in): 1

Ties:

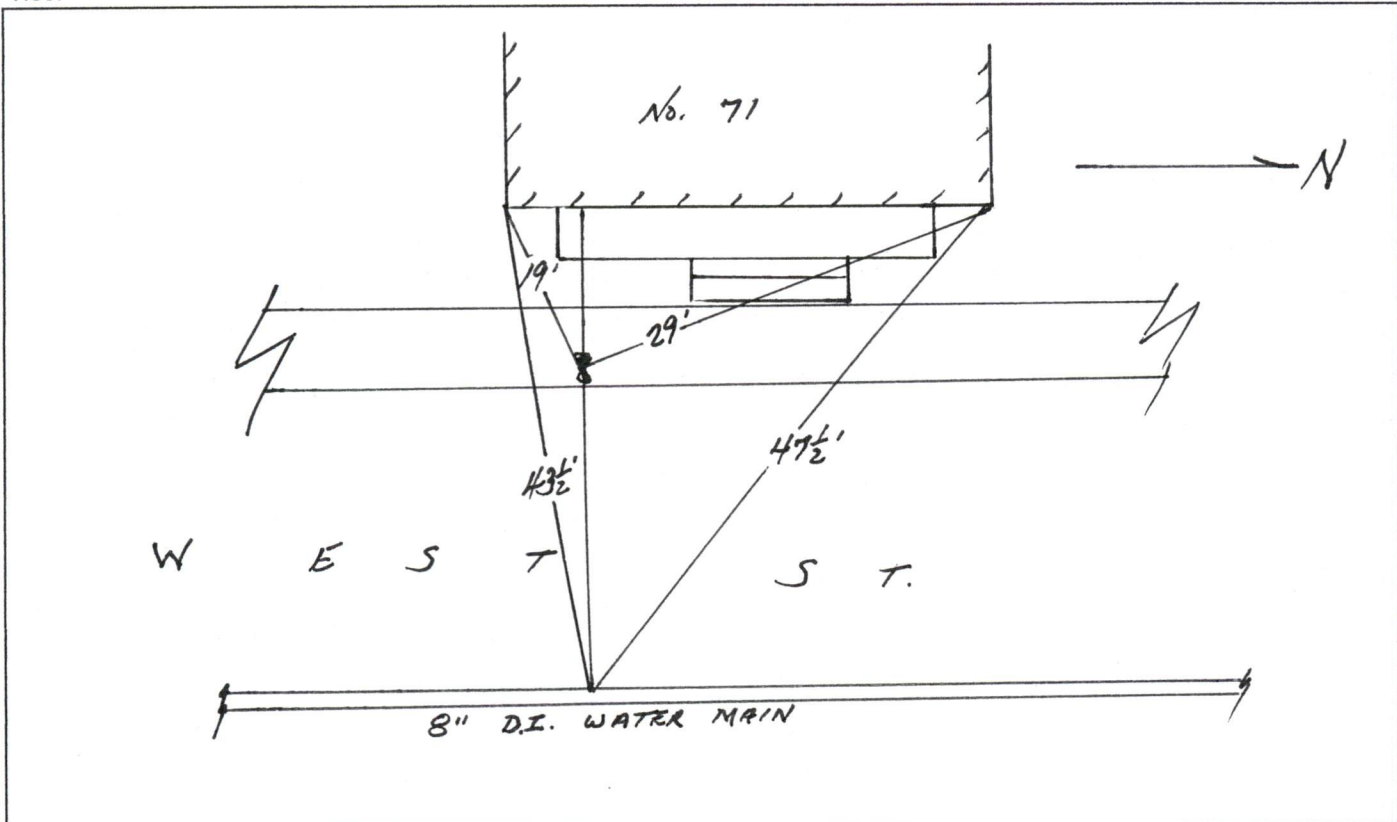

Remarks:

22' $\frac{3}{4}$ " LEAD SERVICE REMOVED.
TYPE C - 1" COPPER TO METER
