

APPLICATION No.: 16129

TAP CLEARED

LOCATION: 349 Earle St

OWNER: _____

31-313

MEASURES: 06/26/2019 - Lead Service Line Replacement

Program, Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 75

Distance from main to curb stop (ft) N/A

Distance from curb stop to meter (Ft) 24

Distance from curb face to curb stop (ft) 2.3

Depth of service (ft) 4

Total length of new pipe installed (ft) 24

Curb stop replaced: no

Corporation replaced: no

Ball Valve Furnished: yes size 1"

DATE


BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

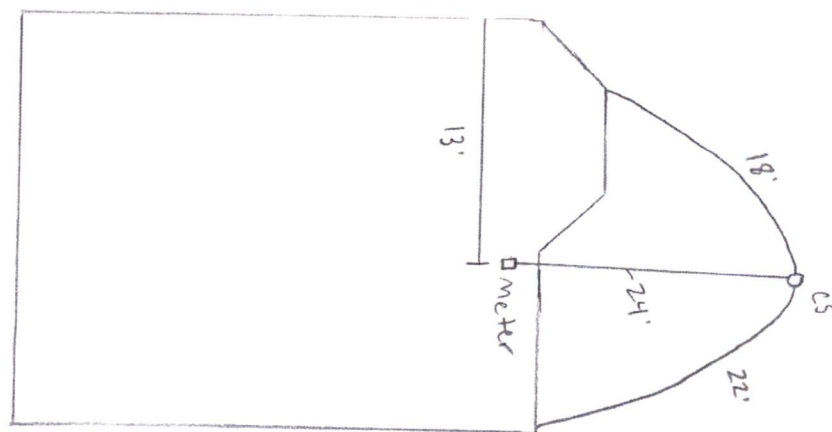

APPLICATION No.: 16129

TAP CLEARED 8323-0081

LOCATION: 349 Earle

OWNER: Antoni Harmot

MEASURES:

5/8"

W from	Brook	193.4
S from N line	Earle	8.5
E from W line	House	10.0

JUN 7 - 1983 -- Renewed 6" outside to 4.6 ft. inside curb stop. 5.0 ft. - 3/4" copper; 3/4" curb stop; stop box; 2- 5/8" x 3/4" lead-cop. adapt. XS;

7/31/86: Renewed from 18" outside of curb stop to 6" outside of curb stop.
1 ft. - 3/4" copper tubing 3/4" x 3/4" cop to cop cplg.
5/8" x 3/4" lead to copper adapt. XXS

Renewed from 9 ft. North of main to a point 12 ft. N x main.
3 ft. - 3/4" copper tubing 1 - 5/8" x 3/4" lead to copper adapt XXS
1 - 3/4" curb stop.

NOTE: TURN OVER FOR MORE INFO ON REPAIRS TO SERVICE

DATE

BEF.

AFT.

REMARKS

9/13/04

Tap reamed

[illegible]

CHARGE OUTS

9/13/04	Renewed from main to property line. Stock: 30 ft. 3/4" copper tubing; 3/4" curb stop; Caldwell stop box; 5/8" x 3/4" lead-cop adapt. XS; 5/8" x 3/4" Fig. 413 Tap reamed
---------	--
