

APPLICATION No.: 16418

LOCATION: 63 CLIFFORD ST.

OWNER: E. Boisvert

31-313

Measures:	5/8"		
	E from	Concord	59.8'
	S from N line	Clifford	9'
	W from E line	House	9.3'

1" Copper Service

08/30/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 24'

Distance from curb stop to meter 20'

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 44'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes N/A

Remarks: Type C -1" Copper to meter, 12' Lead removed.


TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

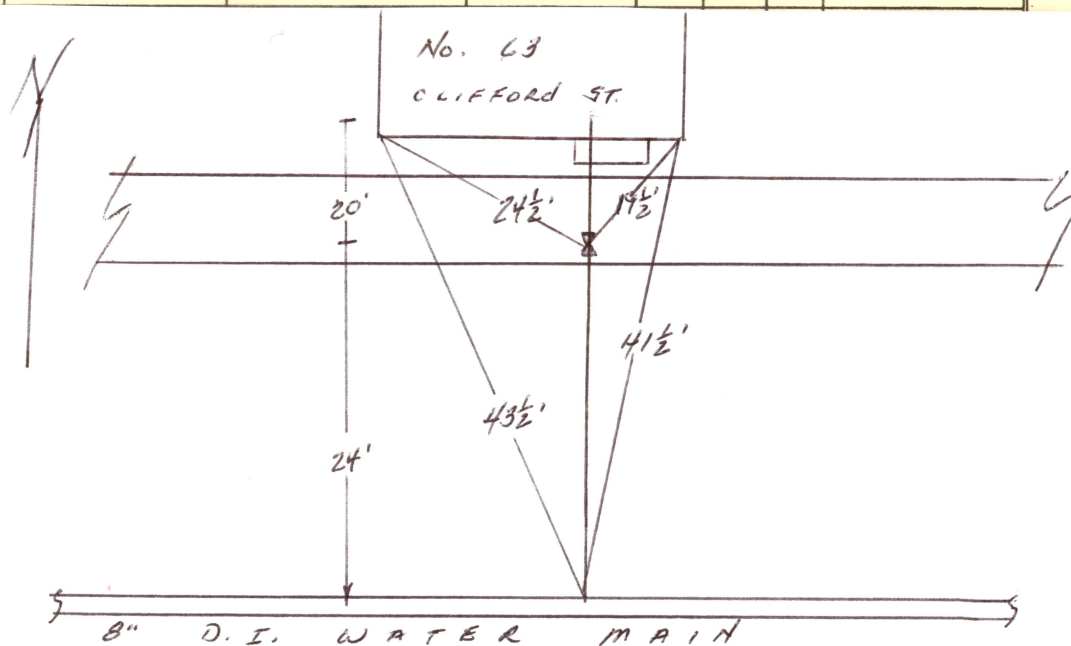[illegible]

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: Clifford ST

HOUSE No: 63

Contractor: C. Naughton Corp.

Date: 8-30-22

Type: CU

Diameter (in):

1

Distance from main to curb stop (ft):

24'

Distance curb stop to meter (ft):

20'

Distance from curb face to curb stop (ft):

1 1/2'

Depth of Service (ft):

4 1/2'

Total length of new pipe installed (ft):

44'

Curb Stop Replaced: Yes

Size (in):

1

Corporation Replaced: Yes


Size (in):

1

Ball Valve Replaced:

Size (in):

Ties:

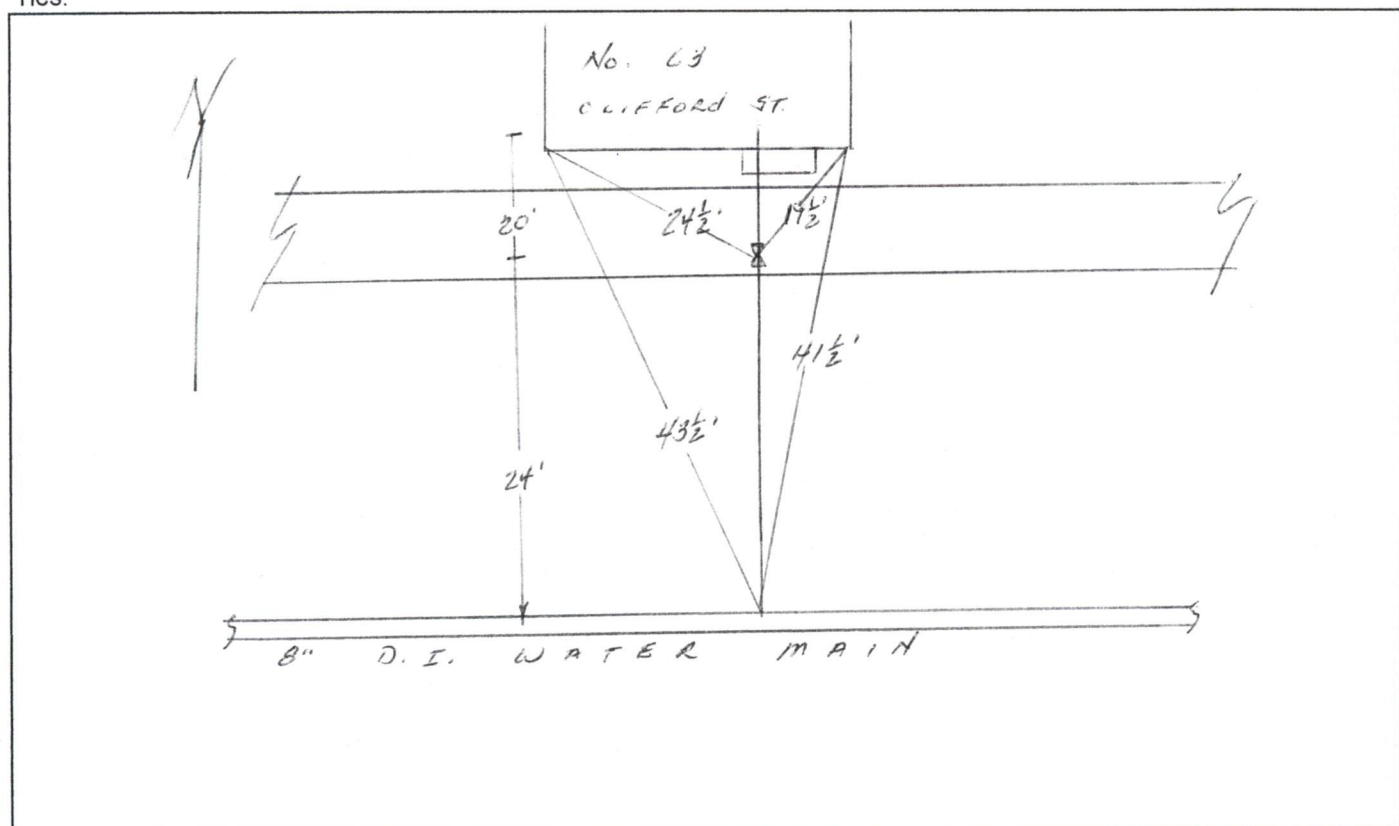

Remarks:

TYPE C - 1" Copper to meter 12' LEAD REMOVED
