

APPLICATION No.: 16548

LOCATION:

OWNER:

31-313

Measures: 5/8"

W from Arlington 19.9'

S from N line	Clifford	8.7'
---------------	----------	------

E from W line House 6.1'

1" Copper Service

09/08/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 23.5'

Distance from curb stop to meter 20'

Distance curb face to curb stop 2'

Depth of Service 4'

Total length of new pipe installed 43.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes N/A

Remarks: Type C-1" Copper to meter 10' Lead pipe removed.

TAP CLEARED

DATE _____

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

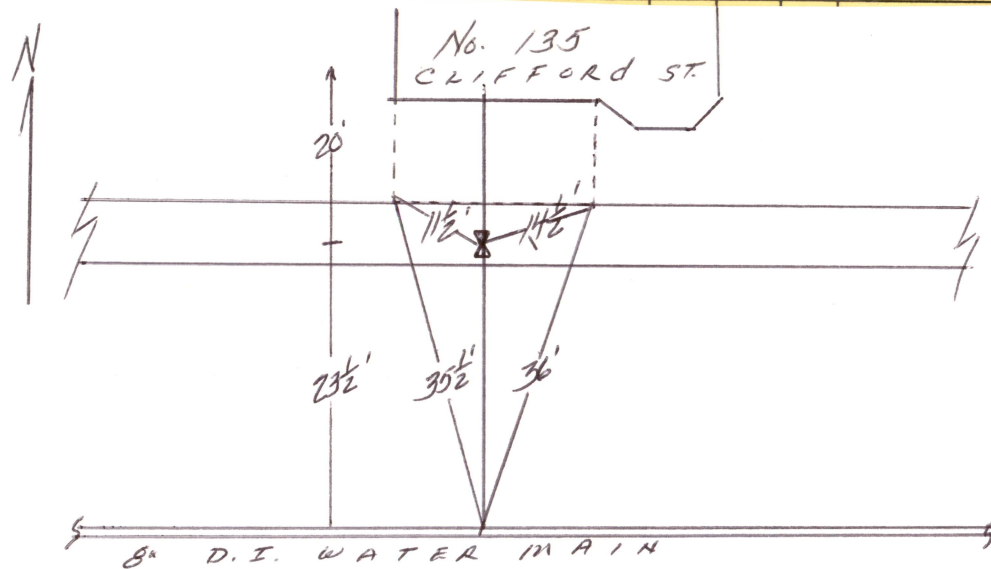

C L I F F O R D S T.
