

17180

LOCATION: 47 Frederick St

OWNER:

31-313

MEASURES: W from E. Rodney French 421.0'
S from N. line Frederick St 7.9'
E from W. line house 8.0'

1" COPPER SERVICE

8-22-2019: Lead service line replacement program
phase 1, Contractor P. Gioioso & Sons, TYPE CU

Diameter 1 inch, Water Pressure 100

Distance from main to curb stop 26'

Distance curb stop to meter 21.7'

Distance from curb face to curb stop 3.0'

Depth of service 4.1'

Total length of new pipe installed 21.7'

Curb stop replaced:NO Size 3/4"

Corporation replaced:NO Size 3/4"

Ball Valve furnished: YES Size 1"

Remarks: 1-3/4" union installed where shown

TAP CLEARED

DATE _____

BEF.

AFT.

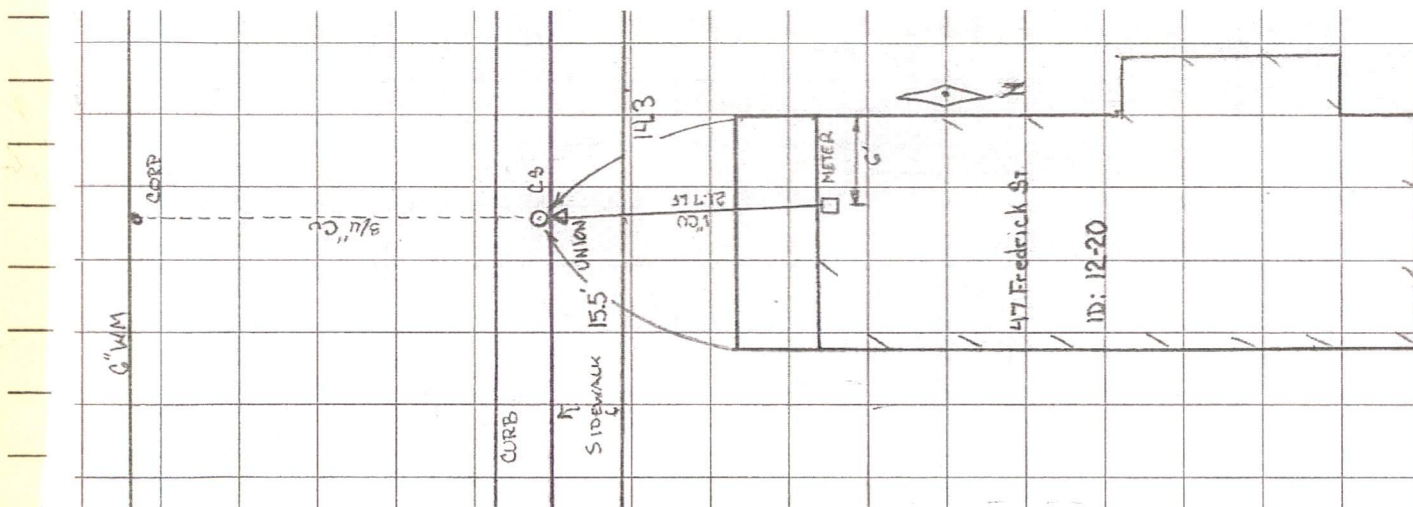
REMARKS

1/28/91:reamed

10/21/93: ream

[illegible]

CHARGE OUTS

[illegible]
