

APPLICATION No.: 17418 5/8"

## TAP CLEARED

LOCATION: 19-21 Clifford St. N.S. W. of Acushnet Ave.

OWNER: Philias Fortin

MEASURES: 5/8"

W from	Acushnet Ave.	170.0 ft.
S from N line	Clifford	8.4 ft.
W from E line	House	2.3 ft.

1/21/80: Renewed from 6" outside curb stop to inside cellar. 20 ft.-3/4" copper (10' inside); 3/4" curbstop; 5/8" x 3/4" lead-cop. adapt. XXS; Caldwell stop box;

12/13/2018: DPI/ Ronnie A. did water repair, replaced service from main to curb stop. (curb stop was broken)  
Lucity # 18-016646

## 1" Copper Service

08/25/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 26.5'

Distance from curb stop to meter N/A

Distance curb face to curb stop 1.5'

Depth of Service 4.5'


Total length of new pipe installed 33.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes 1"

Remarks: Type B - Connect to existing 3/4" Copper @ PL.

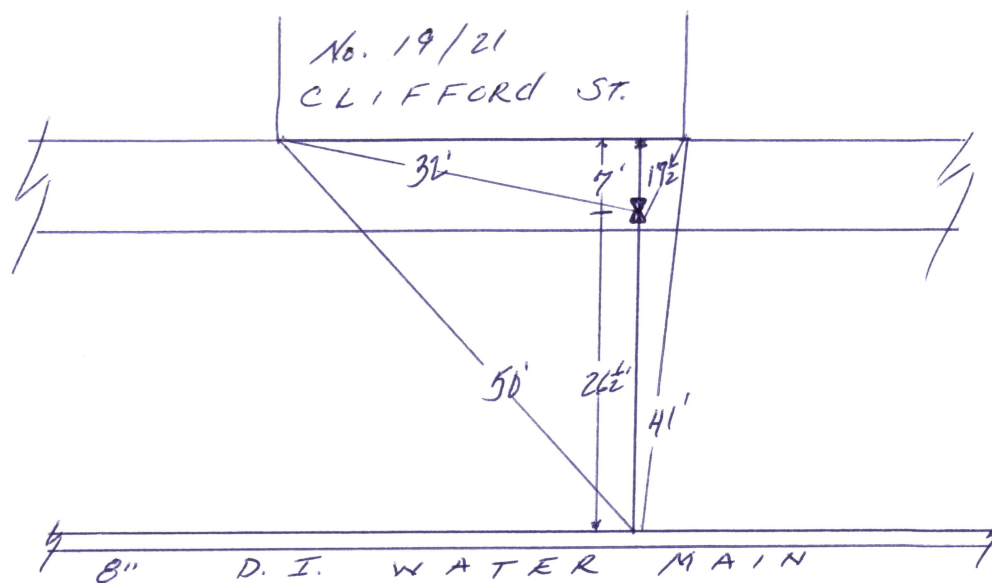[illegible]

C L I F F O R D S T.



## Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: CLIFFORD ST.

HOUSE No: 19 / 21

Contractor: C. Naughton Corp.

Date: 8-25-22

Type: CU

Diameter (in):

1

Distance from main to curb stop (ft):

26.5'

Distance curb stop to meter (ft):

-

Distance from curb face to curb stop (ft):

1.5'

Depth of Service (ft):

4.5'

Total length of new pipe installed (ft):

33.5'

Curb Stop Replaced: Yes

Size (in):

1

Corporation Replaced: Yes

Size (in):


1

Ball Valve Replaced:

Size (in):

1

Ties:

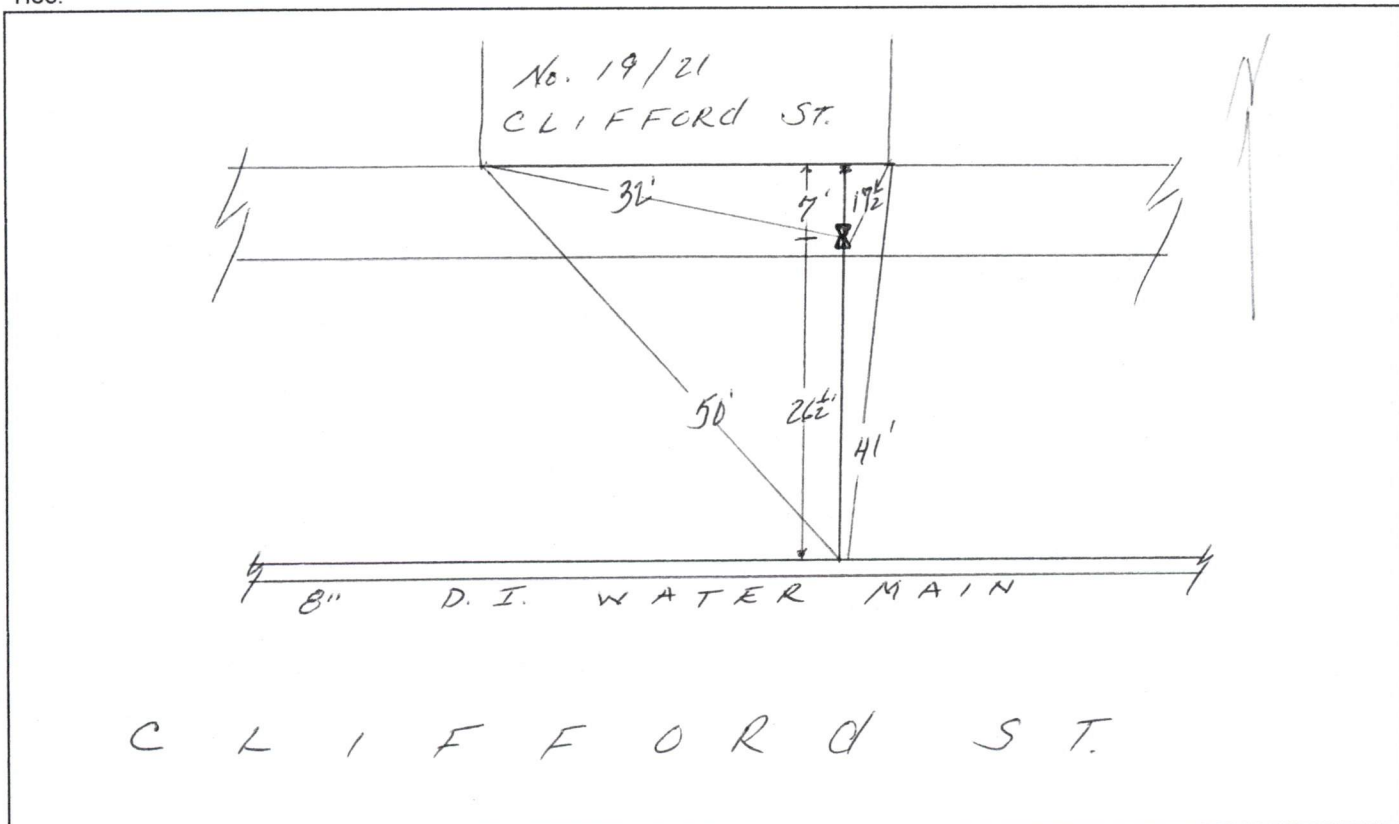

Remarks:

TYPE B - CONNECT TO EXISTING 3/4" COPPER @ #.
