

APPLICATION No.: 1759

LOCATION: 106 South Sixth St

TAP CLEARED

OWNER:

31-313

MEASURES: 1" Copper Service
06/03/2019 Lead Service Replacement Program
Phase 1, Contractor P Gioioso & SOn
Type CU, Diameter 1in, Water pressure 100
Distance from main to curb stop (ft) N/A
Distance from curb stop to meter (ft) 19
Distance from curb face to curb stop (ft) 2
Depth of service (ft) 4.5
Total length of new pipe installed (ft) 19
Curb stop replaced: No
Corporation replaced: No
Ball valve furnished: Yes size 1"

DATE


BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

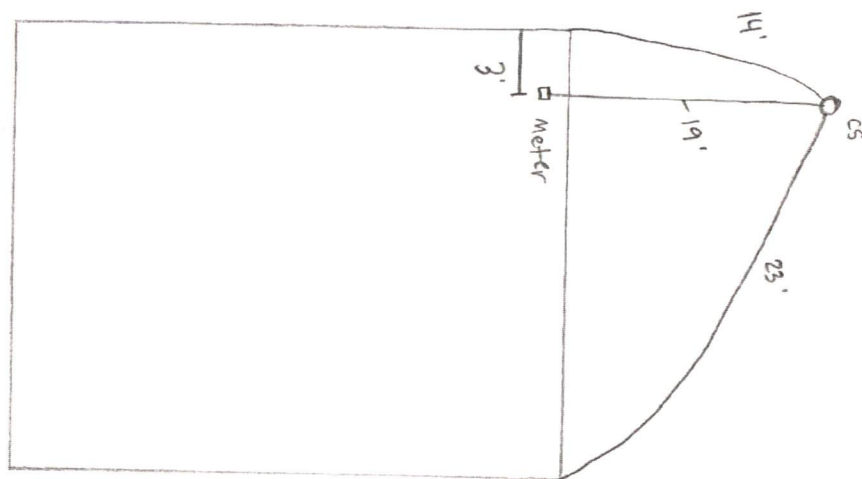

APPLICATION No.: 1759

TAP CLEARED

V

LOCATION: 106 So. Sixth

OWNER: John J Braz

MEASURES: 5/8"

S from

W from E line

N from S line

Wing

Sixth

House

146.7 ft.

6.6 ft.

2.2 ft.

DATE

BEF.

AFT.

REMARKS

1/2/91: TAP REAMED

1- 9016438 T32
9309-1674

 December 29, 1958 Renewed from a point $\frac{1}{8}$ ft. outside curb stop to
 a point 4 ft. inside curb stop.

4 $\frac{1}{8}$ ft. of 3/4" copper tubing 1 3/4" copper stopop
 2 lbs. wiping solder

12/26/90: Renewed from $\frac{1}{2}$ ' outside curb stop to prop line
 Stock: 7ft. 3/4" copper tubing 1-3/4" curb stop
 1- Caldwell stop box 2- 3/4x5/8 lead to cop adapt. xxs

1/2/91: Renewed from main to curb stop-Installed in this order
~~Stock: 18ft. 3/4" copper tubing 1-3/4" curb stop~~
 1- 1/2x3/4 Fig. 413 - flared

1 ft. - 3/4" Copper tubing

1 - 3/4" curb stop (buried)

17 ft. - 3/4" copper tubing - to the curb stop in sidewalk.

[illegible]

CHARGE OUTS

[illegible]
