

APPLICATION No.: 17897

LOCATION: 291 - 293 Nash Rd

OWNER:

31-313

MEASURES: 1" Copper Service

06/04/2018 Lead Service Repolacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 70

Distance from curb stop to main (ft) N/A

Distance from curb stop to meter (ft) 9.5

Distance from curbface to curb stop (ft) 1.3

Depth of service (ft) 3.5

Total length of new pipe installed (ft) 9.5

Curb stop replaced: no Corporation replaced: no

Ball valve replaced: yes size 1"

Remarks: 9.5 ft curb stop to meter

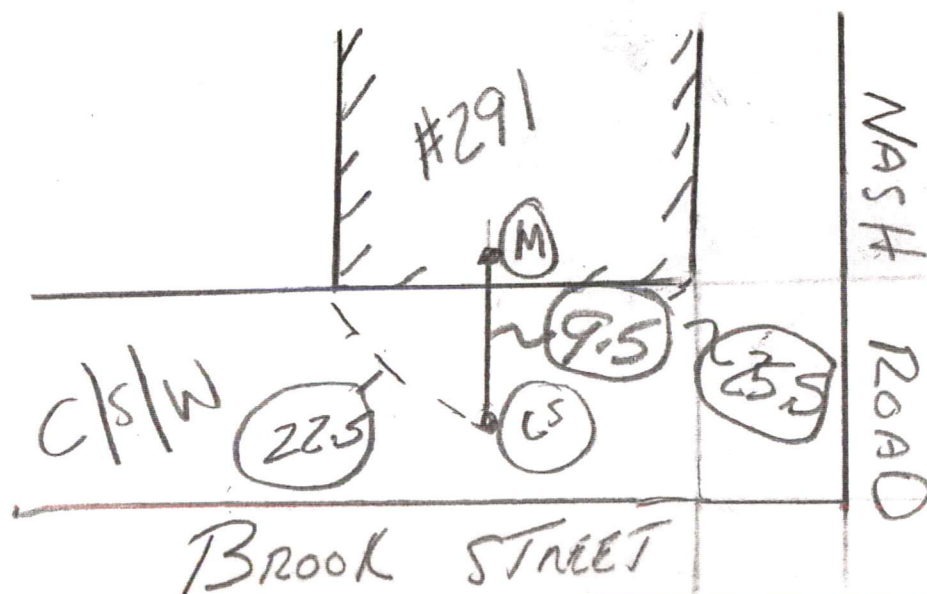
TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

[illegible]

291.

APPLICATION No.: 17897

TAP CLEARED

LOCATION: N.E. Cor. 293 Nash Rd. & BrookOWNER: Gerald FauteuxMEASURES: 5/8"

N from	Nash Rd.	23.6 ft.
W from E line	Brook	9.3 ft.
N from N line	Bldg.	3.6 ft.

DATE

BEF.

AFT.

REMARKS

6/27/02 830 am 2002-260-7474

7/2/02

Reamed tap

February 11, 1960 Service extended 8 ft. inside cellar
8 ft. of 3/4" copper tubing

Stock supplied & installed by owners plumber

Nov. 18, 1976 Renewed from 1/2 ft. outside curb stop to
a point 7 ft. inside curb stop.

7 1/2 ft. - 3/4" Copper tubing 3/4" Curb Stop
Caldwell Stop Box 2 - 5/8" x 3/4" lead connector

July 2, 2002 Renewed from main to curb stop.

25 ft - 3/4" Copper tubing; 3/4" curb stop; Caldwell Stop Box;
5/8" x 3/4" fig. 413

[illegible]

CHARGE OUTS

[illegible]
