

APPLICATION No.: 17909 5/8"

TAP CLEARED

LOCATION: 29-31 Clifford St. N.S. W. of Acushnet Ave.

OWNER: Joseph N. Porier

MEASURES: 5/8"

W from Acushnet Ave.

297.3 ft.

S from N line Clifford

8.6 ft.

E from W line House

8.8 ft.

June 9, 1956 Renewed from property line to inside cellar
12 ft. of 3/4" copper tubing

12-10-98 Renewed from main to property line. Stock:
33 ft. - 3/4" Copper tubing, 1 - 3 7/8" Curb Stop,
1 - Caldwell Stop Box, 1 - 5/8" x 3/4" lead to cop. adapt.
XS, 1 - 5/8" x 3/4" Fig. 413.

1" Copper Service

08/25/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 23.5'

Distance from curb stop to meter N/A

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 28.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"


Ball Valve replaced yes 1"

Remarks: Type B -Connect to existing 3/4" Copper @ PL.

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS
12/12/57		5/8	HERSEY King	533305					

CHARGE OUTS

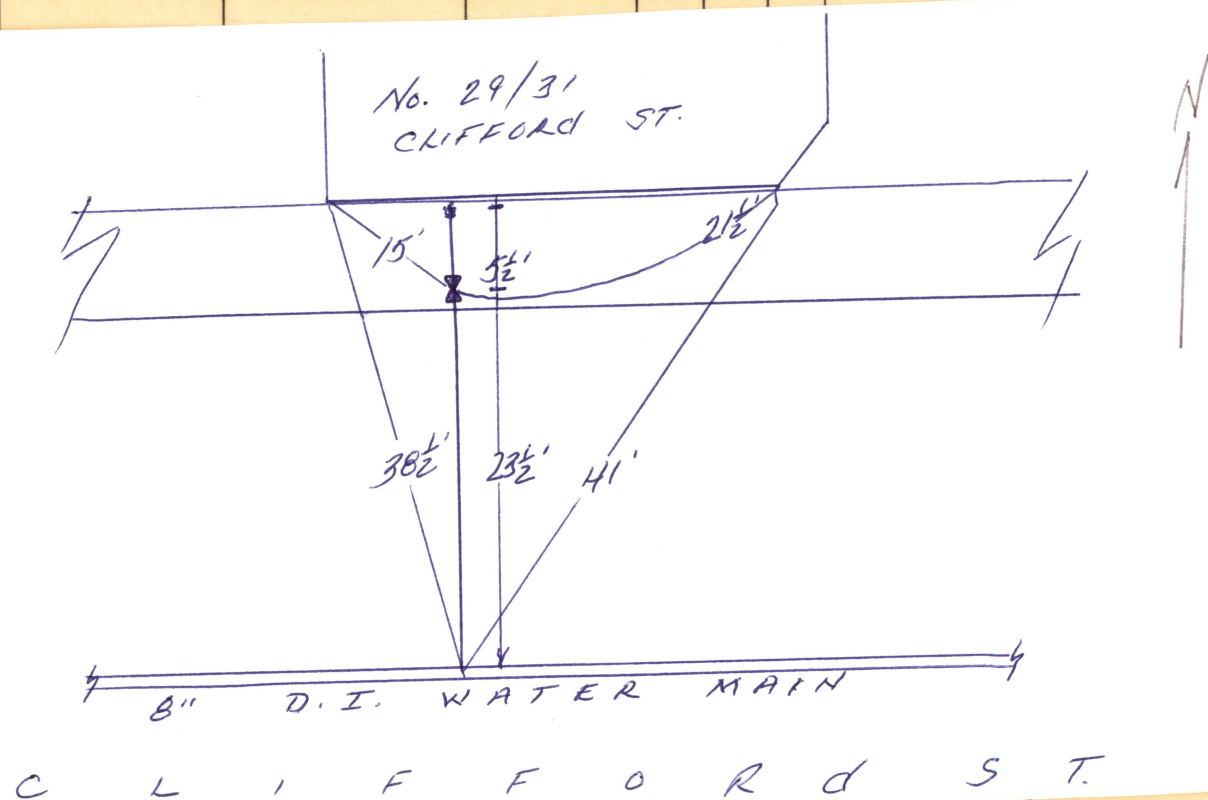

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: CLIFFORD ST

HOUSE No: 29/31

Contractor: C. Naughton Corp.

Date: 8-25-22

Type: CU

Diameter (in):

1

Distance from main to curb stop (ft):

23.5'

Distance curb stop to meter (ft):

—

Distance from curb face to curb stop (ft):

1.5'

Depth of Service (ft):

4.5'

Total length of new pipe installed (ft):

28½'

Curb Stop Replaced: Yes

Size (in): 1


Corporation Replaced: Yes

Size (in): 1

Ball Valve Replaced:

Size (in): 1

Ties:

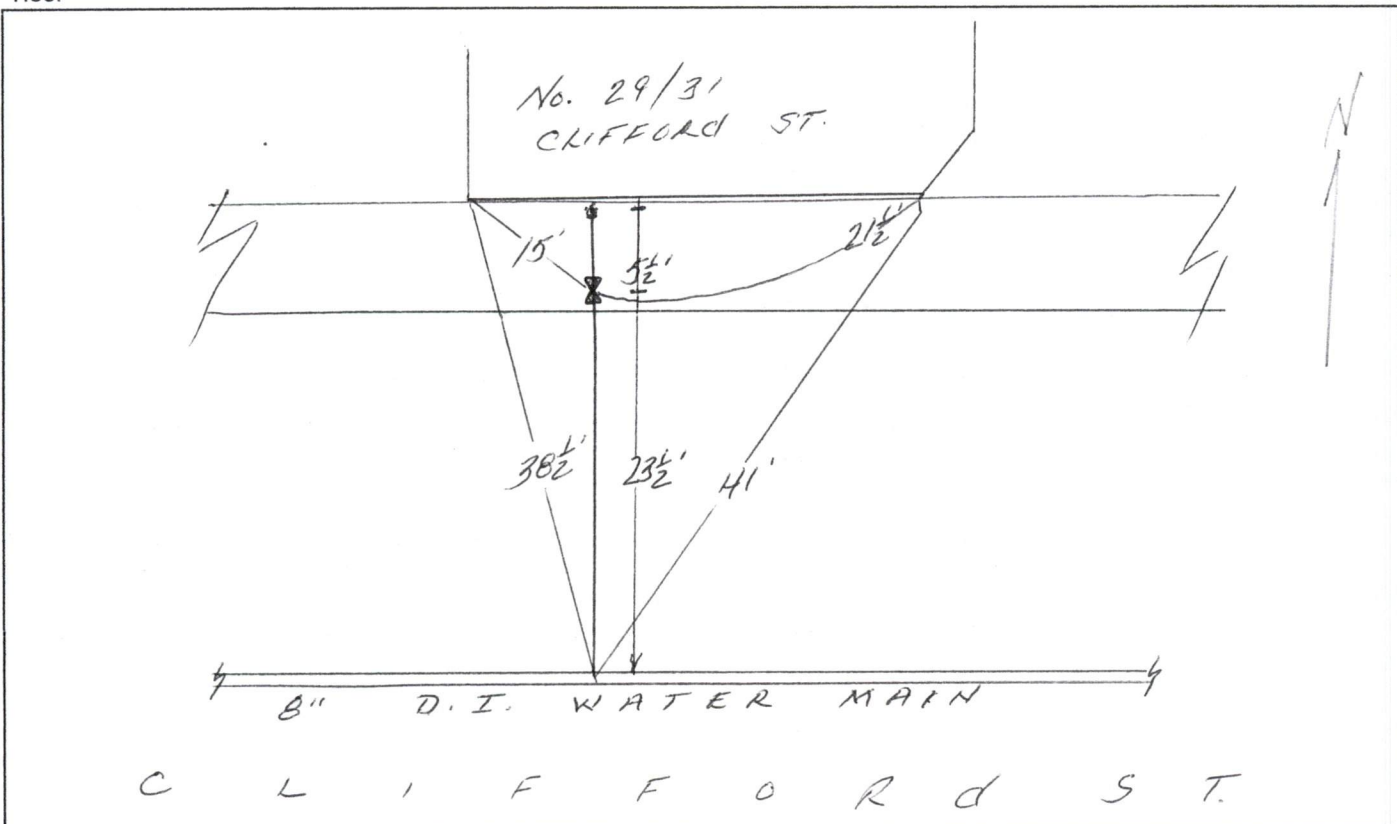

Remarks:

TYPE B - CONNECT TO EXISTING 3/4" COPPER @ 12.
