

APPLICATION No.: 17933

TAP CLEARED

LOCATION: 1070 Cove Rd

OWNER: ✓

31-313

MEASURES: April 12, 1921

E X Stapleton St 84.3 ft

S X Nline Cove Rd 3.4 ft

E X W line House 11.0 ft

1" Copper Service Replacement Program Phase 1"

Contractor Gioioso and Sons

Type CU, Diameter (in) 1, Water pressure 100

Distance from main to curb stop (ft) 23

Distance curb stop to meter (ft) 23.4

Distance from curb face to curb stop (ft) 2.9

Depth of service (ft) 3.7

Total length of new pipe installed (ft) 23.4

Curb stop replaced: no size 3/4"

Corporation replaced: no, size 3/4"

Ball valve furnished: yes, size 1"

Remarks: 1-3/4" union installed 1 lf outside curb stop

DATE _____

BEF.

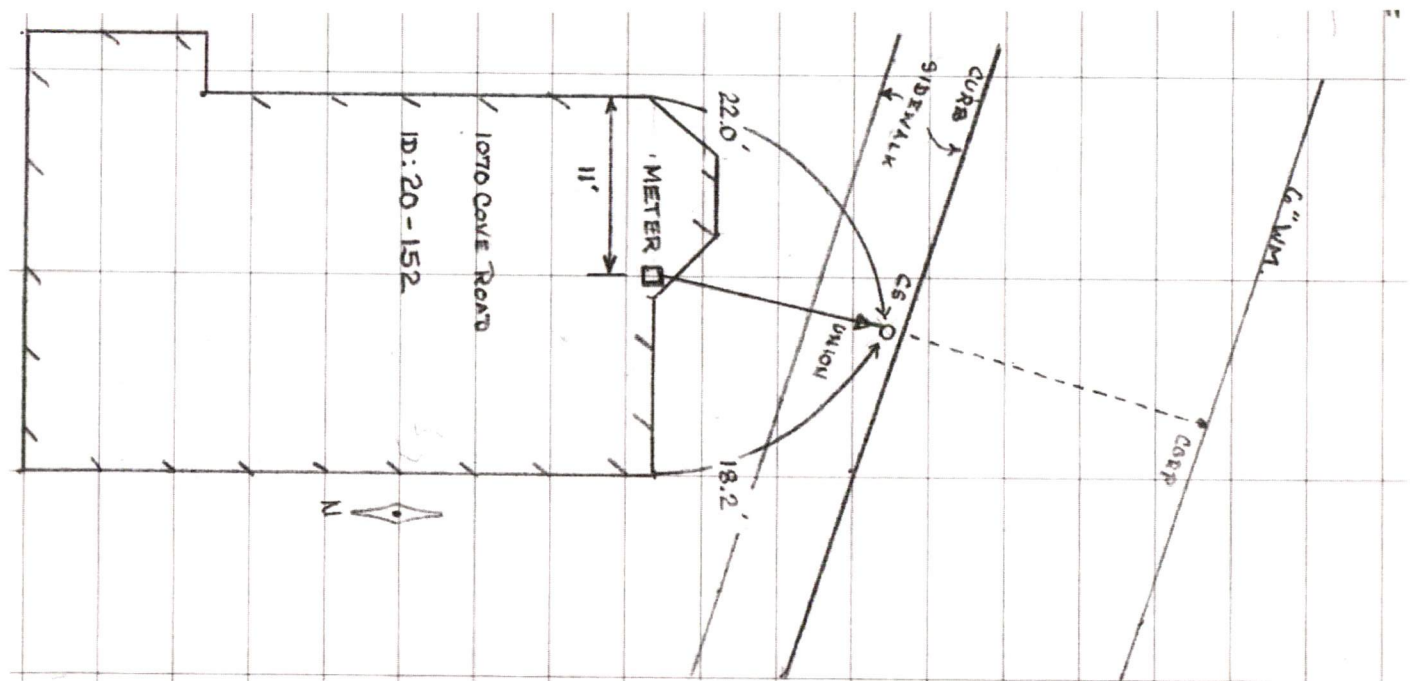
AFT.

REMARKS

3/23/72 Ream

[illegible][illegible]

CHARGE OUTS

[illegible]
