
APPLICATION No.: 17953 TAP CLEARED LOCATION: 159 CliffORD ST.

Alfred Codier DATE AFT. REMARKS 5/8" Measures: E from Ashley Blvd 226' S from N line Clifford 9' E from W line House 13' 1" Copper Service 09/13/2022 2022 Water main improvement program Contractor: C. Naughton Corp. Type CU Diameter 1" Distance from main to curb 22.5' Distance from curb stop to meter N/A Distance curb face to curb stop 2' Depth of Service 4' Total length of new pipe installed 45.5' Curb Stop replaced yes size 1" Corporation replaced yes 1" Ball Valve replaced yes N/A Remarks: Type C-1" Copper to meter 12' of Lead pipe removed.

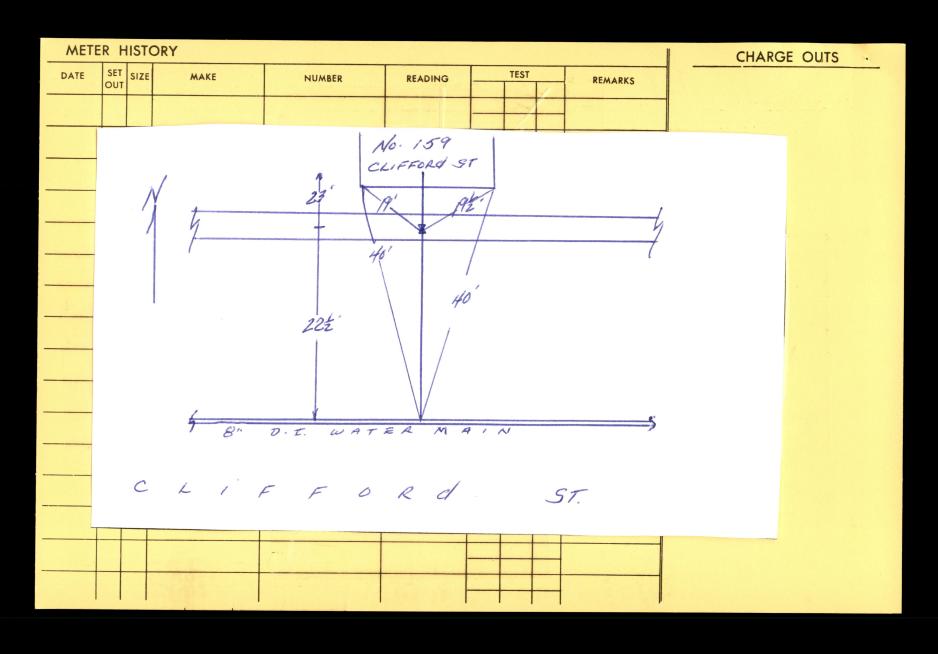

APPLICATION No.: 17953 5/8"	TAP CLEARED 51 0813			
LOCATION: 159 Clifford St. N.S.E. of Ashley Blvd.	DATE	BEF.	AFT.	REMARKS
OWNER: Alfred Codier				
			3 4	
MEASURES: 5/8" E from Ashley Blvd. 226.0 ft. S from N line Clifford 9.0 ft.				
S from N line Clifford 9.0 ft. E from W line House 13.0 ft.	100			
E from W line House 13.0 ft.				
Dec. 21, 1983 - Renewed from 6" outside curb stop to				
a point 6½ ft. inside curb stop. 7 ft 3/4" copper tubing 1 - 3/4" curb stop 2 - 5/8" x 3/4" lead to copper adaptors XS				
1 - 3/4" curb stop 1 stop box				
2 - 5/8" x 3/4" lead to copper adaptors XS				
			Name of the second	
			*	
				•
	1			

METER HISTORY							CHARGE OUTS		
DATE	SET	SIZE	MAKE	NUMBER	READING	-	TEST	REMARKS	
3/22/62		5/8		533387					
							1		
					1				
	-								
				* .	•				
	1000	27.511							
