

APPLICATION No.: 18370 3/4"

TAP CLEARED 8949-0057

LOCATION: 4080 Acushnet Ave.

OWNER: A. J. Blankeron

MEASURES: 3/4"

N from

Braley Rd.

512.8 ft.

W from E line

Acushnet Ave.

6.0 ft.

N from S line

House

11.8 ft.

Dec. 4, 1989 renewed from 1/2 ft. outside curb stop to a point  
3 ft. ins. of curb stop.

4 ft. - 3/4" copper tubing 1 - 3/4" curb stop 1 stop box

2 - 5/8" x 3/4" lead to cop adapt XXS

-----  
10-23-98 Replaced broken curb stop. Stock: 1 - 3/4"  
Curb Stop.  
-----

11/02/07 - NE Pressure Project - Tied service into  
new 12" water main. Renewed from main to property  
line

Stock: 36 ft -3/4" copper tubing; 1 -3/4" curb stop;  
1 Caldwell stop box; 1 -5/8" x 3/4" lead to cop  
adapt. xxs; Note: This service is under 12" high  
pressure gas main in sidewalk area. Foreman: F. Bento  
12/18/17: Lead service line replacement program,  
Contractor: P. Gioioso & Sons

Type: CU, Diamter 1, Water Pressure 60  
Distance from main to cur l stop: N/A

Distance from cur l face to cur l stop 4.0'

Depth of service 4'  
cur l stop replaced NO: size 3/4"  
corporation replaced NO: size 3/4"  
Ball valve furnished YES: size 1"

DATE

BEF.

AFT.

REMARKS


10/22/98

284307441

# METER HISTORY

# CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

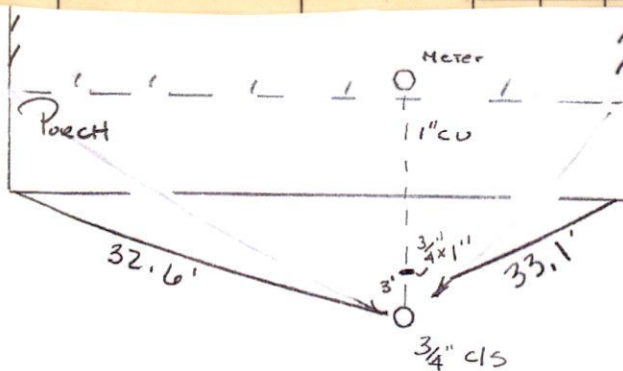

Rosa Dr.

Acushnet Ave
