

APPLICATION No.: 18648

TAP CLEARED

LOCATION: 19 County St 19-21

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: 5/2/2019 - Lead Service Line Replacement Program

Phase 1 Contractor P Gioioso & Son

1" Copper Service

Type CU, Diameter (in) 1, Water Pressure 100

Distance from main to curb stop(ft) N/A

Distance curb stop to meter (ft) 15

Distance from curb face to curb stop (ft) 4

Depth of service (ft) 4

Total length of new pipe installed (ft) 15


Curb stop replaced: No

Corporation replaced: No

Ball valve furnished: Yes, size 1"

[illegible]

CHARGE OUTS

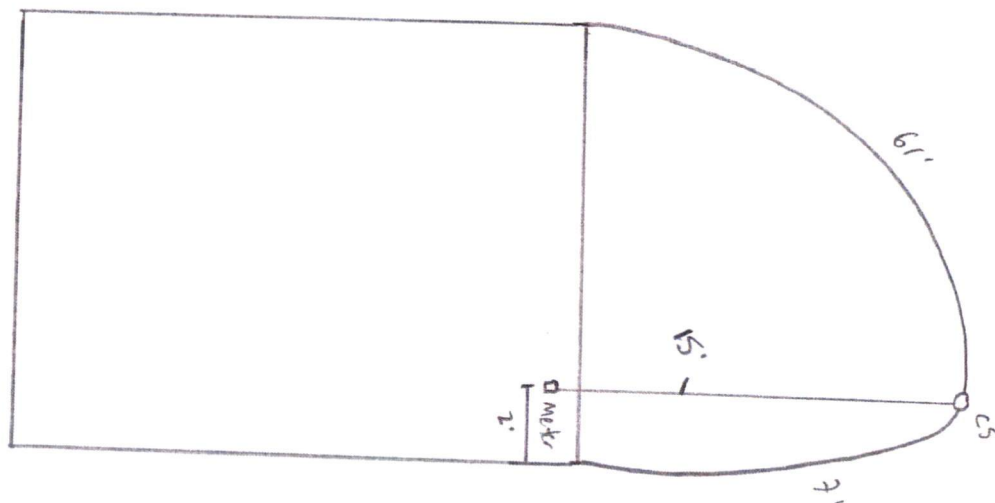

APPLICATION No.: 18648

TAP CLEARED

LOCATION: 19-21 County St.

OWNER: Alexander Pelletier, Et Ux P.20-4.113

MEASURES: 5/8"

H lead June 7, 1922

N from S line

COVE RD
Brook Ave. E 4.0 ft.

E from W line

County St. 4.0 8-6 ft.

N from N line

bldg. 4.0 ft.

May 7, 1975 Renewed from the main to 1 ft. inside property line.

19 ft. - 3/4" Copper tubing

3/4" Curb Stop

Caldwell Stop Box

5/8" x 3/4" Fig. 413

5/8" lead to copper adaptor XXS

Owner was not in the bldg. -Could not renew into cellar

DATE

BEF.

AFT.

REMARKS

5/7/75

Reamed

[illegible]

CHARGE OUTS

APPLICATION No.: 21005 6" Cast Iron

TAP CLEARED

LOCATION: 19-21 County St.

OWNER:

MEASURES: 6"

Cast Iron

Nov. 10, 1925

Darling Gate Tron Box.

N from Cove Rd.

15.6 ft.

E from W line

County

17.3 ft.

N from S line

Bldg.

15.5 ft.

FIRE SUPPLY

METER HISTORY

[illegible]

CHARGE OUTS*
