

APPLICATION No.:

TAP CLEARED



LOCATION: 89 - 91 Clara St

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES:

Dec. 2, 1922

E from Cleveland St 400.3 ft

S from N line Clara St. 9.0 ft

W from E line House 12.4 ft

1" Copper Service

09/10/2019 Lead Line Service Replacement

Program Phase 1 Contractor P. Gioioso and Son

Type CU, Diameter (in) 1, Water Pressure 100

Distance from main to curb stop (ft) 25

Distance curb stop to meter (ft) 28

Distance from curb face to curb stop (ft) 2

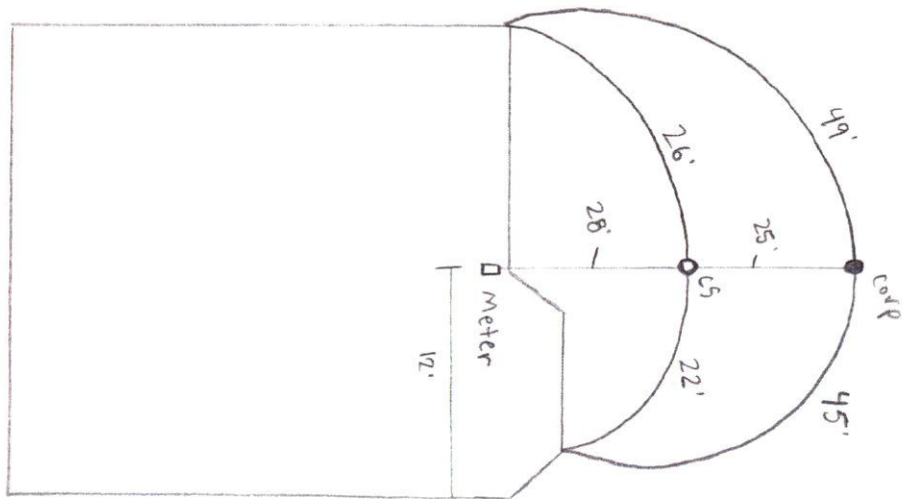
Depth of service (ft) 3.8

Total length of new pipe installed (ft) 53

Curb stop replaced: Yes, Size 1"

Corporation replaced: yes, Size 1"

Ball Valve furnished: Yes, Size 1"

[illegible][illegible]
