

APPLICATION No.: 19459

TAP CLEARED

LOCATION: 1207 Cove Rd

OWNER: ✓

31-313

MEASURES: 1" Copper Service

7/9/2019 Lead Service Line Replacement Program

Phase 1, Contractor P. Gioioso & Son

Type:CU, Diameter (in) 1, Water Pressure 100

Distance from main to curb stop (ft) n/a

Distance curb stop to meter (ft) 22

Distance from curb face to curb stop (ft) 1

Depth of service (ft) 4

Total length of new pipe installed (ft) 22

Curb stop replaced: no, corporation replaced: no

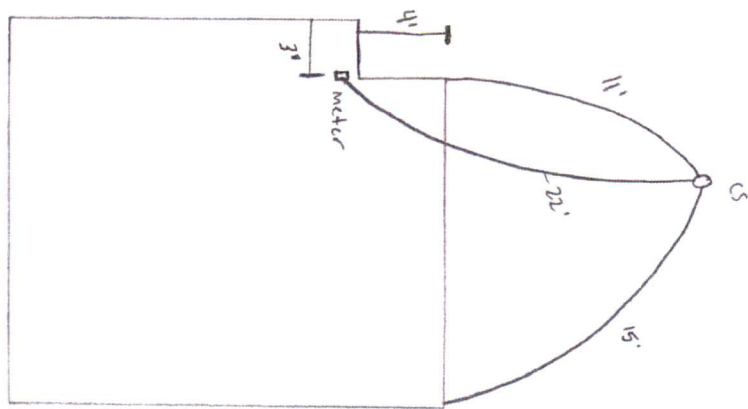
Ball valve furnished: yes, 1"

DATE

BEF.

AFT.

REMARKS

[illegible]

APPLICATION No.: 19459

TAP CLEARED 88/7-0071

LOCATION: 1207 Cove Rd.

OWNER: Antone Francis

MEASURES: 5/8" H lead May 25, 1923

E from Crapo St. 426.2 ft.

S from N line Brock Ave. 9.6 ft.
Cove Rd. 7.1

W from E line house 12.8 ft.

October 29, 1974 Renewed from the main to a point 7½ ft.
inside curb stop.17½ ft. - 3/4" copper tubing 3/4" Curb stop
5/8" lead to copper adaptor 3/4" x 3/4" Fig. 413
XXS Caldwell Stop Box

Contractor supplied all stock except Stop Box

Due to the widening of Cove Rd. the curb stop was
relocated 2½ ft. northerly.J 4/25/88: Reset curb stop box. - - -

DATE

BEF.

AFT.

REMARKS

[illegible]

CHARGE OUTS

[illegible]
