

APPLICATION No.: 19531 5/8"

TAP CLEARED

LOCATION: 164-66 Belleville Rd.

OWNER: Frank Souza

MEASURES: 5/8" L.L.

W from Acushnet Ave. 310.8 ft.

N from S line Belleville Rd. 8.8 ft.

E from W line House 3.0 ft.

Sept. 8, 1977: Renewed from 6" outside curb stop to prop.
line. 10½ ft. - 3/4" copper; 2-3/4" x 3/4" lead to cop.
adapt. XS; 3/4" curb stop; Caldwell stop box;

Sept. 11, 1996: STREET RECONSTRUCTION

Renewed from main to curb stop

Stock: 9.7ft 3/4" copper tubing same curb stop
same Caldwell stop box 1-3/4x5/8 Fig 413

Insp. M Rose A Olejarz TILCON EXCAVATION

4/2/2018 LEAD SERVICE LINE REPLACEMENT PROGRAM Phase 1
CONTRACTOR GIOIOSO

TYPE: CU DIAMETER 1'

distance from main to c/s n/a

c/s to meter 19.5'

curbface to c/s 1.0'

depth of service 4.2'

total length of new pipe installed 22.5'

c/s replaced-no Corporatio replaced ;no

Ball valve furnished ;yes 1"

DATE

BEF.

AFT.

REMARKS


9/11/96: tap reamed

METER HISTORY

CHARGE OUTS

| DATE | SET OUT | SIZE | MAKE | NUMBER | READING | TEST | | | REMARKS |
|------|------------|------|------|--------|---------|------|--|--|---------|
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |

Ties:

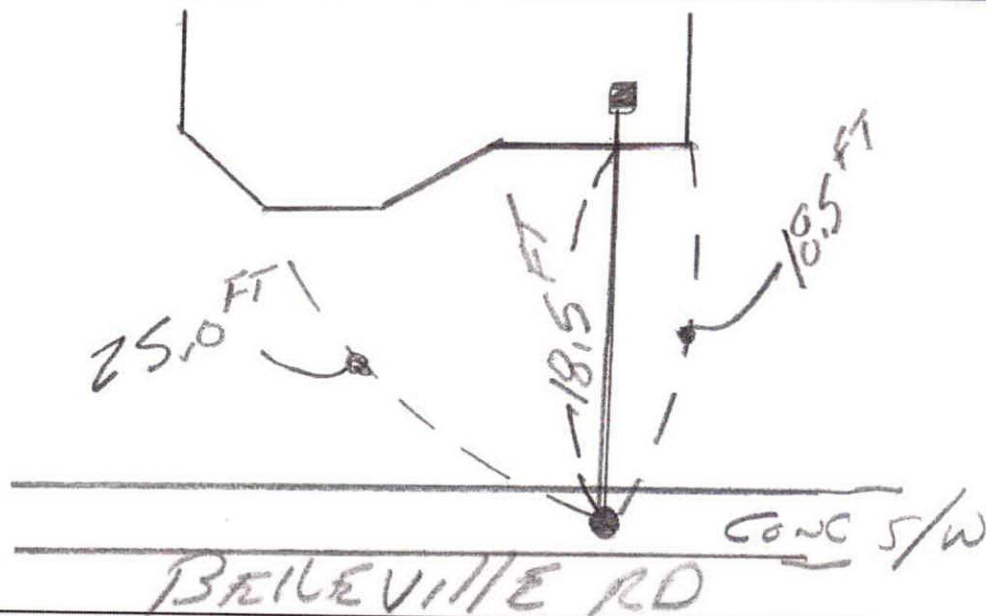

Remarks:

APPLICATION No.:

TAP CLEARED

LOCATION:

OWNER:

31-313

MEASURES:

18.5 ft curbstop to face of house
1.0 ft wall thickness
3.0 whip
total 22.5 1" copper

DATE

BEF.

AFT.

REMARKS

METER HISTORY

[illegible]

CHARGE OUTS
