

4263

APPLICATION No.: 19559

TAP CLEARED

LOCATION: N.W. Cor. Acushnet Ave. & June

OWNER:

MEASURES:

3/4"

COPPER

N from

June

22.2 ft.

E from W line

Acushnet Ave.

7.8 ft.

N from S line

house

9.6 ft.

3/1

3/12/18: Lead service line replacement program
 contractor: P. Gioioso & Son
 Type: CU, Diameter 1"

Distance from main to curb stop N/A

Distance curb stop to meter 28'

Distance from curb face to curb stop 2.0'

Depth of service 3.8'

Total length of new pipe installed 28.0'

Curb stop replaced N/A

corporation replaced N/A

Ball valve furnished yes : Size 1"

New 1" copper length includes 3ft interior connection to water meter.

DATE

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

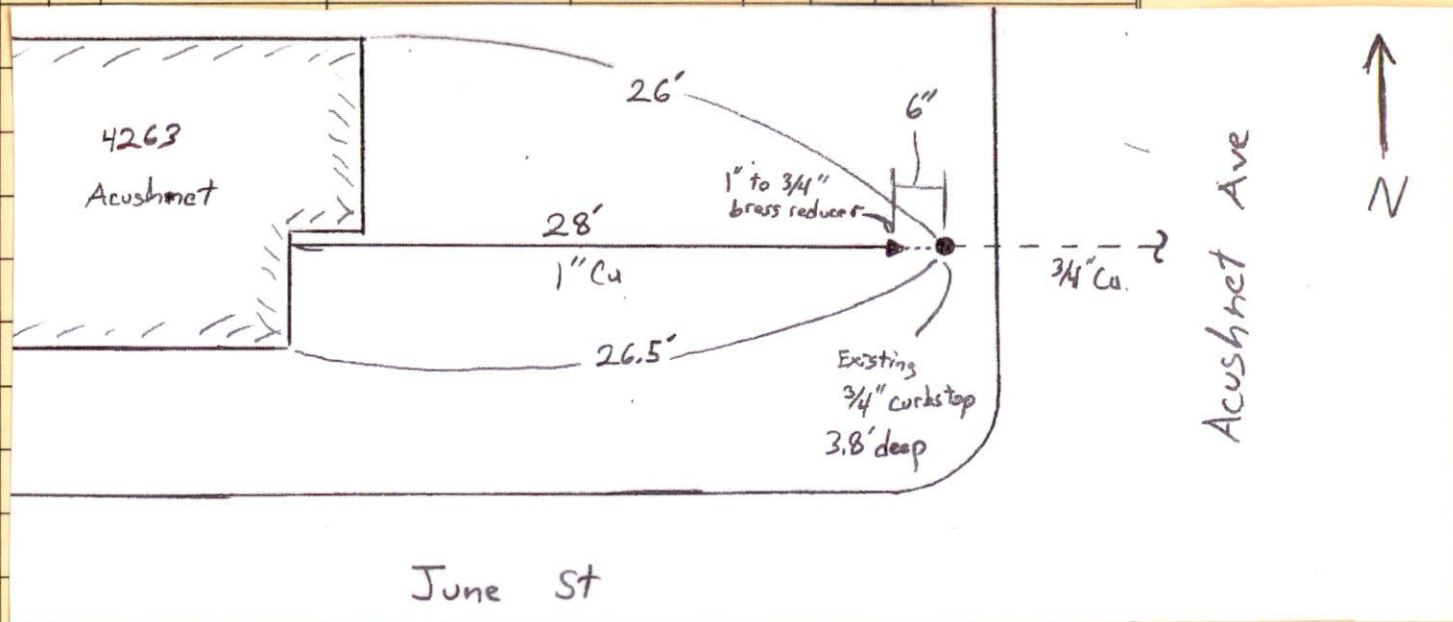

APPLICATION No.: 19559 3/4"

TAP CLEARED

LOCATION: 4263 Acushnet Ave.

OWNER: M. R. Sasseville

MEASURES:

3/4"

N from

June St.

22.2 ft.

E from W line

Acushnet Ave.

7.8 ft.

N from S line

House

9.6 ft.

Nov. 25, 1980: Renewed from 6" outside curbstop to the property line.

5 ft.-3/4" copper

1-3/4" curb stop 1-Caldwell stop box

2-5/8" x 3/4" lead-cop. adapt. XXS

2-25-2000 Renewed from main to curb stop. Stock:

9 ft. - 3/4" Copper tubing, 1 - 3/4" Curb Stop,

1 - Caldwell Stop Box, 1 - 3/4" x 3/4" Fig. 413.

8/26/08 - North End Pressure Project - City tied service into new 12" water main

8 ft - 3/4" copper tubing; 1 - 3/4" cop to cop cplg. comp

Foreman: Danny Perry

Second Card ->

DATE

BEF.

AFT.

REMARKS

2-25-00 20000903496

2-25-2000 Tap reamed

METER HISTORY

[illegible]

CHARGE OUTS
