

APPLICATION No.: 19785

TAP CLEARED

LOCATION: 975 Oakley St

OWNER:

31-313

MEASURES: E X Acushnet Ave 195.2 ft
S X N Line Oakley St 6.2 ft
E X W Line House 0.6 ft

1" Copper Service

03/01/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 55

Distance from main to curb stop (ft) 22.5

Distance from curb stop to meter (ft) 21.8

Distance from curb face to curb stop (ft) 3

Depth of service (ft) 4

Total length of new pipe installed (ft) 22.5

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

Ball valve replaced: No size 3/4"

Remarks: 1-3/4 union installed 0.7" inside
curb stop

DATE

BEF.

AFT.


REMARKS

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST		REMARKS

CHARGE OUTS

Ties:

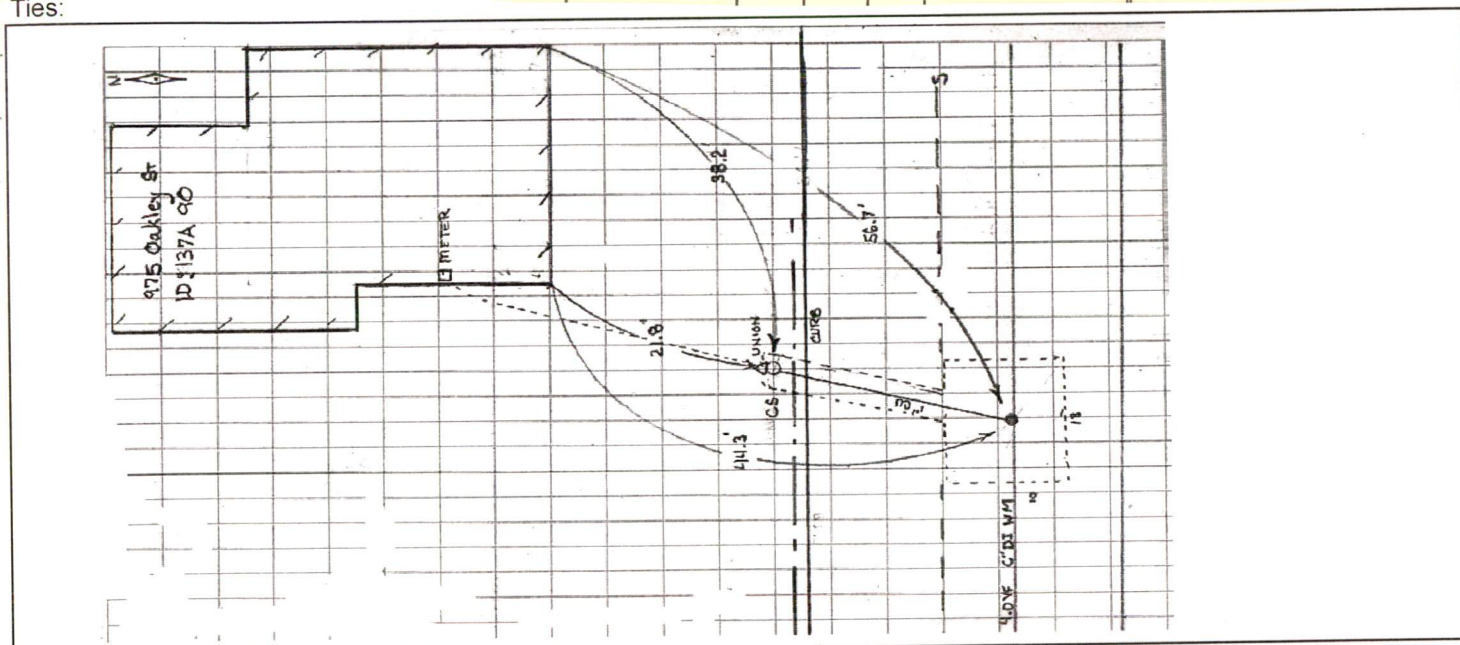

Remarks:
