

19840

228 - 230 Hersom St

OWNER:

31-313

MEASURES: W X Conduit St

N X S Line Hersom St

# E X W Line House

## 1" Copper Service

04/25/2019 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in. Water pressure 85

Distance from main to curb stop (ft) 8

Distance from curb stop to meter (ft) 24

Distance from curb face to curb stop (ft) 3.2

Depth of service (ft) 3.6

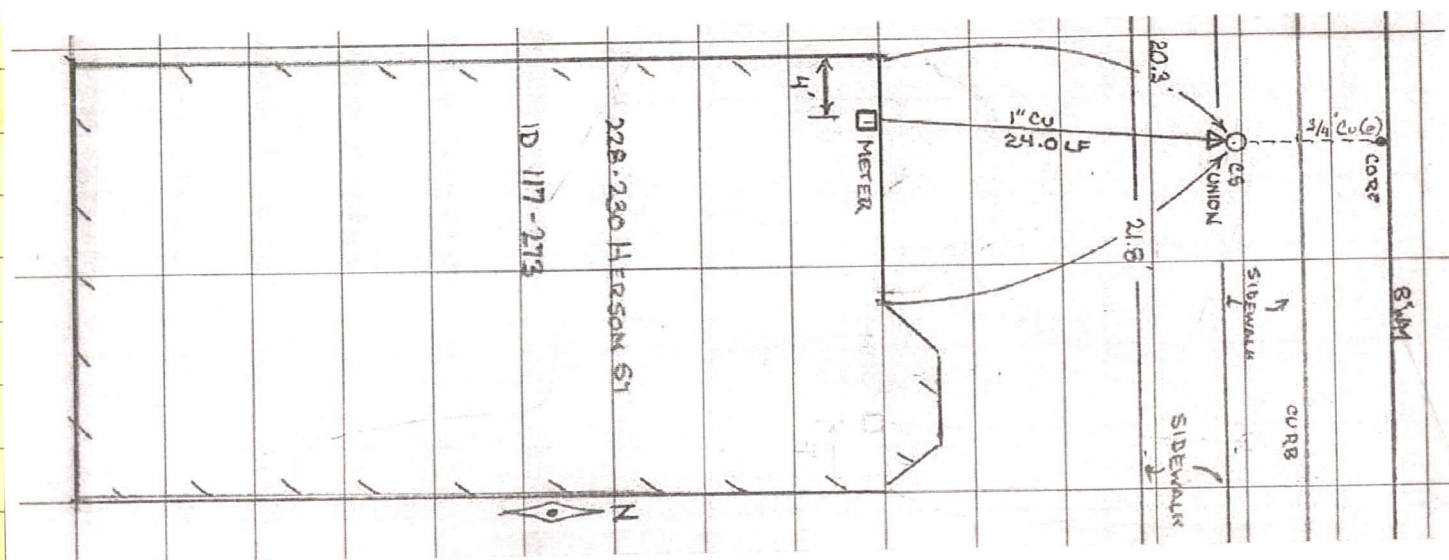
Total length of new pipe installed (ft) 24

Curb stop replaced: no size 3/4"

Corporation replaced: no size 3/4"

Ball valve furnished: yes size 1"

Remarks: 1 - 3/4" union installed 1 ft outside curb stop

[illegible][illegible]
