

APPLICATION No.: 20019

TAP CLEARED

LOCATION: 34 - 36 Covell St

DATE

BEF.

AFT.

REMARKS

OWNER: V

31-313

MEASURES:

W X Belleville Ave 384.4 ft

N X S line Covell St 9.2 ft

W X E line House 5.4 ft

1" Copper Service

5/28/2019 Lead service line replacement program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter (in)1, Water Pressure 100

Distance main to curb stop (ft) 11.6

Distance curb stop to meter (ft) 20.6

Distance curb face to curb stop (ft) 1.5

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 32.2

Curb stop replaced: yes, size 1"

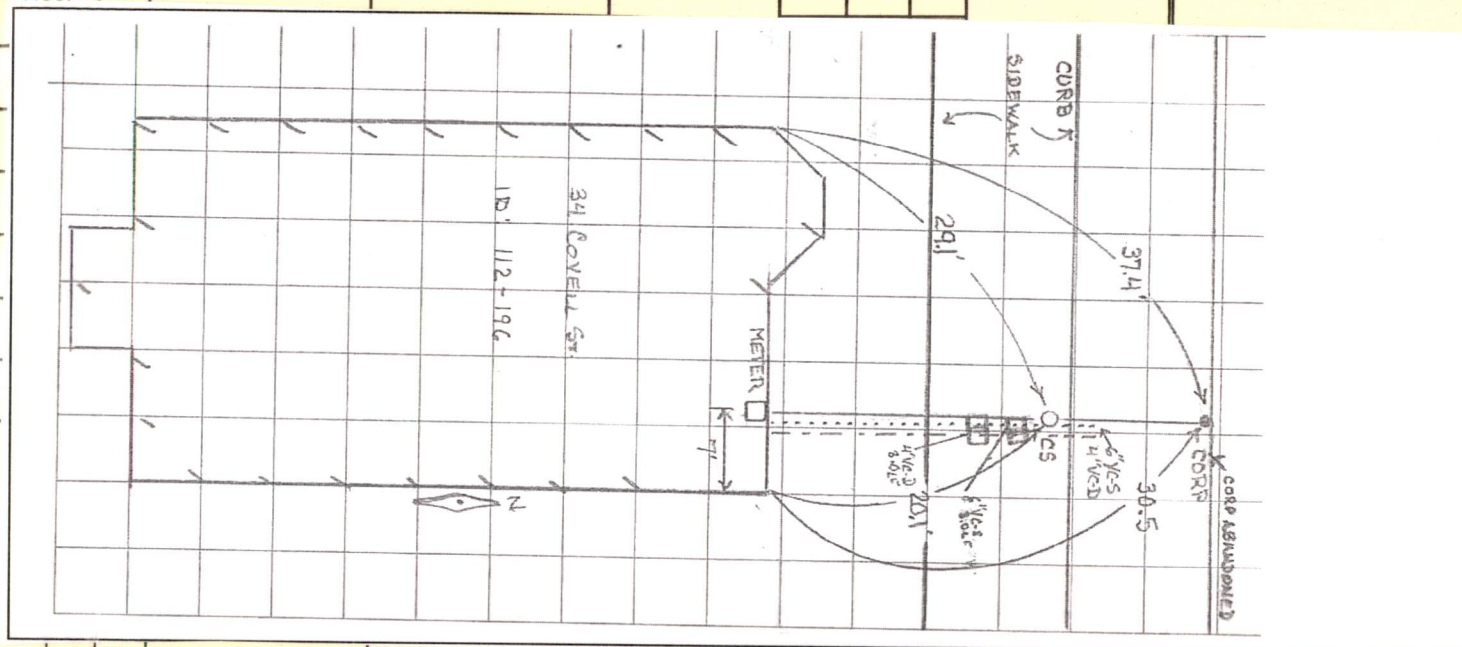
Corporation replaced: yes, size 1"

Ball Valve replaced: yes 1"

Remarks: Existing corp abandoned

[illegible]

CHARGE OUTS

[illegible]
